
### PROVIDENT



**Construction Updates** 

December 2022

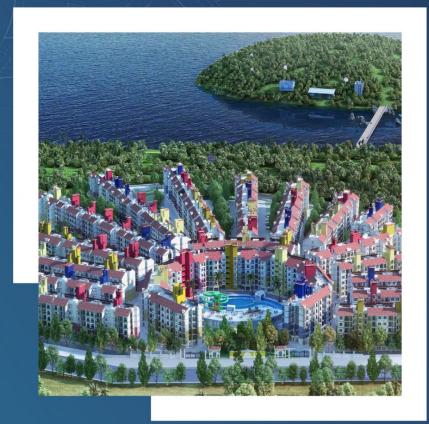

Dear Esteemed Customer,

Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Adora de Goa. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Adora de Goa





### **Provident Adora de Goa**

Dabolim at Central Goa



**Construction Updates** 

Overall view

**18ABC** 

18D

Actual site photograph

#### **PROGRESS TIMELINE**



October 22

#### **TOWER STATUS**

18EFG

- Tower 18A external painting, internal painting works, staircase and passage putty.
- Tower 18B external painting, internal painting works, staircase and passage putty.
- Tower 18C internal doors installation and main door installation work in progress.
- Tower 18D gypsum completed, internal doors and main door work in progress.
- Tower 18E windows installation, lift-well, lobby, painting / putty completed.
- Tower 18F flooring, toilet dado & railing completed. Windows installation completed.
- Tower 18G OHT, gypsum, flooring, toilet dado & flooring completed.



#### **MILESTONES ACHIEVED**

- 18A,B,C,D,E,F,G Lift well, staircase and lobby completed.
- 18A,B,C,D,E,F,G -External plumbing completed.



#### **UPCOMING MILESTONES**

18A,B,D,E,F,G - Fixing of sanitary fittings and main doors.



Actual site photograph

# TOWER STATUS

- Tower 17AC2 Internal doors and painting in progress. Main door installation in progress.
- Tower 17BC4 External painting works in progress.
- Tower 17CC2 Painting in progress, flats internal doors installation completed.



#### MILESTONES ACHIEVED

 T17A,B,C – lift well, staircase and lobby works completed.



# UPCOMING - MILESTONES

 T17A,B,C - Fixing of sanitary fittings and main doors.



### **Tower 16AC5**



Actual site photograph

### TOWER STATUS

- Above terrace works completed.
- Gypsum work completed.
- Flooring work in progress.



### MILESTONES ACHIEVED

• Terrace slab completed.



# UPCOMING MILESTONES

• Completion of flooring & windows.



### **Tower 15AC5**



Actual site photograph

# TOWER STATUS

- Above terrace works are in progress.
- Gypsum work completed.
- Flooring works completed.
- Toilet dado works in progress.
- Cornice work in progress.



# MILESTONES ACHIEVED

• Flooring & windows completed.



# UPCOMING MILESTONES

• Completion of external plumbing, elevation & terrace waterproof.



### **Tower 14AC5**



Actual site photograph

# TOWER STATUS

- Above terrace works are in progress.
- Gypsum works completed.
- Cornice completed.
- Flooring works in progress.



# MILESTONES ACHIEVED

• Terrace slab completed.



# UPCOMING MILESTONES

• Completion of flooring & windows.



### **Tower 13AC5**



Actual site photograph

# TOWER STATUS

- Flooring completed.
- Gypsum completed.
- Cornice works in progress.



#### MILESTONES ACHIEVED

• Construction of walls, internal plaster, flooring and windows completed.



# UPCOMING MILESTONES

• Completion of external plumbing and external plaster, elevation and terraces (with waterproofing).



### **Tower 12AC6 & BC3**



Actual site photograph

# TOWER STATUS

- Tower 12AC6 gypsum & flooring completed, toilet dado, windows completed.
- Tower 12BC3 external paint one coat putty, vitrified flooring, railing, gypsum & UPVC doors & windows installation completed, toilet dado & toilet flooring completed.



#### MILESTONES ACHIEVED

- T12A completion of external plumbing and external plaster, elevation and terraces(with waterproofing).
- T12B Staircase lobby and lift well.



# UPCOMING MILESTONES

- T12A Completion of sanitary fitting and main door.
- T12B Completion of sanitary fitting and main door.



### **Tower 11AC6**



Actual site photograph

# TOWER STATUS

- Above terrace works completed.
- Flooring & gypsum completed.
- Toilet, balcony and utility flooring works completed.
- Painting works in progress.



### MILESTONES ACHIEVED

• External plumbing and external plaster, elevation and terraces (with waterproofing) completed.



# UPCOMING MILESTONES

• Fixing of sanitary fittings and main doors.



#### 10ABC



Actual site photograph

#### **PROGRESS TIMELINE**



#### TOWER STATUS

- Tower 10AC4 above terrace work completed, windows fixing completed. Flooring & gypsum completed.
  Painting work in progress.
- Tower 10BC6 above terrace works completed, flooring completed. UPVC door & windows installation completed. Painting work in progress.
- Tower 10CC3 above terrace, toilet dado, balcony flooring and UPVC door & windows completed. Painting work in progress.



#### MILESTONES ACHIEVED

 T10A,B,C - External plumbing and external plaster, elevation and terraces (with waterproofing) completed.



# UPCOMING MILESTONES

 T10A,B,C Fixing of sanitary fittings and main doors.



Actual site photograph

# TOWER STATUS

- Tower 9AC6 terrace slab completed. Above terrace works in progress.
- Tower 9BC6 first slab work in progress.



# MILESTONES ACHIEVED

• Tower 9AC6 terrace slab completed.



# UPCOMING MILESTONES

- Tower 9AC6 completion of internal walls and windows.
- Tower 9BC6 plinth beam completion.



8BA



8CD

Actual site photograph

# TOWER STATUS

- Tower 8AC2 Above terrace work.
- Tower 8BC5 1st slab is in progress.
- Tower 8CC6 Excavation completed.
- Tower 8DC3 Walls up to plinth beam in progress.



#### MILESTONES ACHIEVED

- Tower 8BC5 completion of plinth.
- Tower 8AC2 terrace slab completed.



# UPCOMING MILESTONES

- Tower 8AC2 flooring & windows.
- Tower 8BC5 2nd slab completion.
- Tower 8CC6 plinth completion.
- Tower 8DC3 plinth completion.



#### **7ABCD**



Actual site photograph

# TOWER STATUS

- Tower 7AC6 terrace slab completed.
- Tower 7BC6 terrace slab is in progress.
- Tower 7DC3 terrace slab completed.
- Tower 7CC6 first floor slab in progress.



# MILESTONES ACHIEVED

- Tower 7DC3 terrace slab completed.
- Tower 7BC6 fourth slab completed.
- Tower 7AC6 terrace slab completed.
- Tower 7C plinth completed.



# UPCOMING MILESTONES

- Tower 7BC6 completion of terrace slab.
- Tower 7CC6 completion of 2nd slab.



September 22

October 22

November 22

December 22

6A 6BCDE



Actual site photograph

#### TOWER STATUS

- Tower 6AC4 gypsum works completed. Waterproofing works in progress.
- Tower 6BC4 gypsum works completed. Waterproofing works in progress.
- Tower 6CC5 terrace above terrace work in progress tower 6DC6 above terrace work in progress.
- Tower 6EC3 above terrace work in progress.



#### MILESTONES ACHIEVED

- 6AC4 terrace slab completed
- 6CC5 terrace slab completed.
- 6DC5 terrace slab completed.



# UPCOMING MILESTONES

- 6AC4 completion of flooring and windows.
- 6BC4 completion of flooring and windows.





Actual site photograph

### TOWER STATUS

- Tower 5AC5 terrace slab completed.
- Tower 5BC5 above terrace and waterproofing work in progress.
- Tower 5CC5 terrace slab completed.
- Tower 5DC3 above terrace work in progress.



#### MILESTONES ACHIEVED

- Tower 5AC5 terrace slab completed.
- Tower 5BC5 terrace slab completed.
- Tower 5CC5 terrace slab completed.



# UPCOMING MILESTONES

 Tower 5AC5 and 5BC5 completion of flooring & windows.



4CBA 4D





Actual site photograph

#### **TOWER STATUS**

- Tower 4AC4 above terrace works completed.
- Tower 4BC4 OHT in progress. Gypsum completed.
- Tower 4CC6 terrace slab completed.
- Tower 4DC3 third slab in progress.



#### **MILESTONES ACHIEVED**

- Tower 4BC4 Terrace slab completed.
- Tower 4CC6 Terrace slab completed.
- Tower 4DC3 Second slab.



#### **UPCOMING MILESTONES**

- Tower 4AC4 & 4BC4 flooring & windows completion.
- Tower 4CC6 flooring and windows completion.
- Tower 4DC3 4th slab completion.

#### **PROGRESS TIMELINE**



October 22

November 22

#### 3DCBA



Actual site photograph

### **PROGRESS TIMELINE**



September 22

October 22

November 22

**TOWER** 

**STATUS** 

completed.

Tower 3A waterproofing

works completed. Waterproofing in progress.

works in progress. Tower 3D above terrace

works in progress.

Tower 3B above terrace

Tower 3C above terrace

#### **MILESTONES ACHIEVED**

- Tower 3A&B terrace slab completed.
- Tower 3D terrace slab completed.
- Tower 3C terrace slab completed.



### **UPCOMING MILESTONES**

- Tower 3A&B flooring & windows completion.
- Tower 3D completion of flooring & windows.
- Tower 3C completion of flooring & windows.

2AB



# TOWER STATUS

- Tower 2A above terrace works completed waterproofing works completed. Flooring work in progress.
- Tower 2B above terrace works completed. Gypsum and waterproofing completed. Flooring work in progress.



# MILESTONES ACHIEVED

- Tower 2B terrace slab completed.
- Tower 2A terrace slab completed.



# UPCOMING MILESTONES

- Tower 2A flooring & windows completion.
- Tower 2B flooring & windows completion.

Actual site photograph



1A

1B

Actual site photograph

# TOWER STATUS

- Tower 1A first slab concrete completed. 2nd slab work in progress.
- Tower 1B 1st slab completed.



# MILESTONES ACHIEVED

- Tower 1B plinth completed.
- Tower 1A plinth completed.



# UPCOMING MILESTONES

- Tower 1A completion of 2nd slab.
- Tower 1B completion of 2nd slab.



### **Mixed – Use Commercial**



**TOWER STATUS** 

- MUC First slab is in progress.
- MUC Plinth completed.

Actual site photograph



### Other activities

#### Clubhouse

#### The Blu Area



Actual site photograph

# TOWER STATUS

- STP-1 slab completed. Waterproofing works in progress.
- UG sump slab completed. Waterproofing works in progress entrance portal external plaster in progress.
- Compound wall grill fixing in progress.
- Blu area excavation done PCC in progress.
- STP-2 PCC work in progress.
- Road excavation, retaining wall & drains work in progress.
- Club house plastering and blockwork in progress.



### Contact Us



#### **Site Office:**

**Provident Adora de Goa** 

Sy.No.198, Zuari Nagar, Vidhyanagar Colony, Chicalim, Goa – 403726.

### **Regional Office:**

Provident Housing Limited No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

**Email**: <a href="mailto:crm@providenthousing.com">crm@providenthousing.com</a> (Subject line – Project name/ unit number)

**Call Us:** +91 - 80-67724001 / 1 860 208 0000

Web: www.providenthousing.com

#### **RERA Registration Number:**

RERA No.: PRGO02190645 (ROW 5 & 6)

RERA Nos.: PRGO02180009 (Row 10,11 & 12), PRGO07180544 (Row 13)

PRGO07180560 (Row 14), PRGO07180561 (Row 15)
