

 PROVIDENT
ADORA DE GOA

Construction Updates
July 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Adora de Goa. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.


Team Provident Adora de Goa

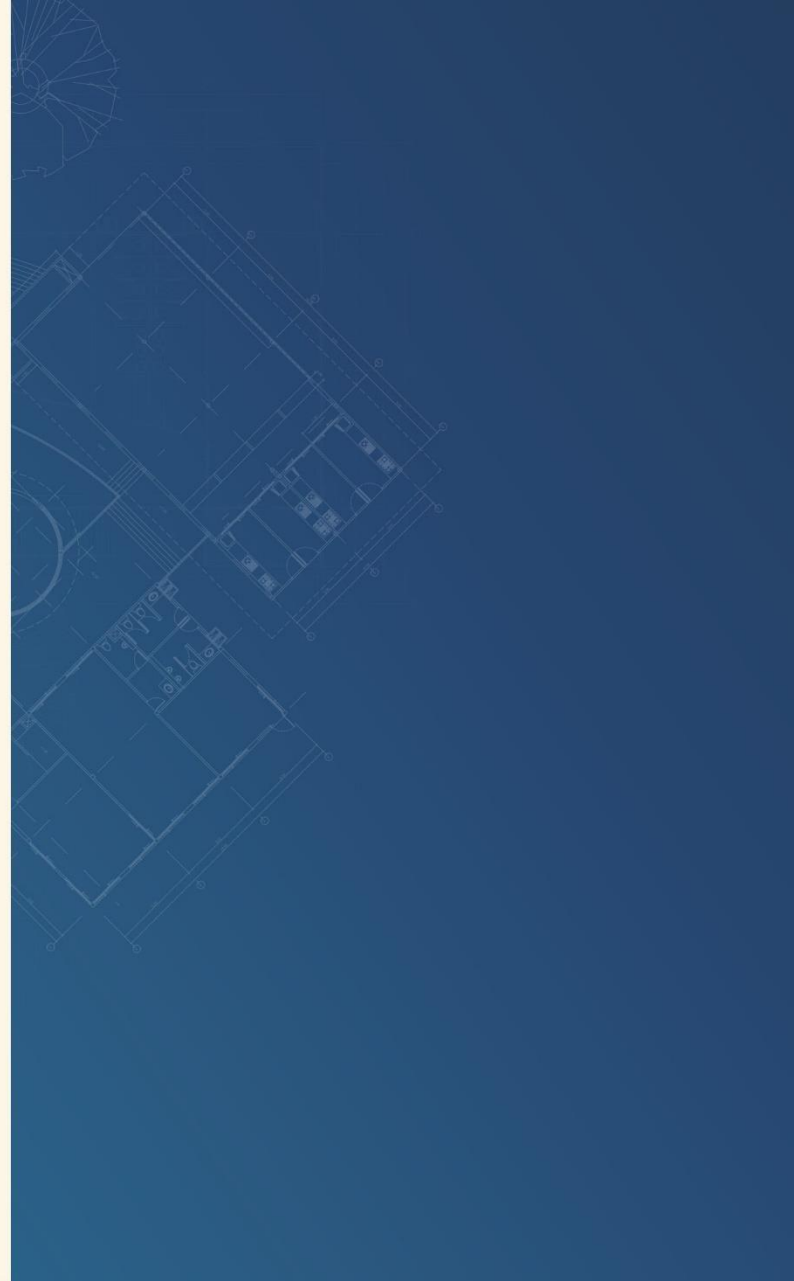



Provident Adora de Goa

Dabolim at Central Goa




Construction Updates

Overall view

BLU AREA




Actual site photograph

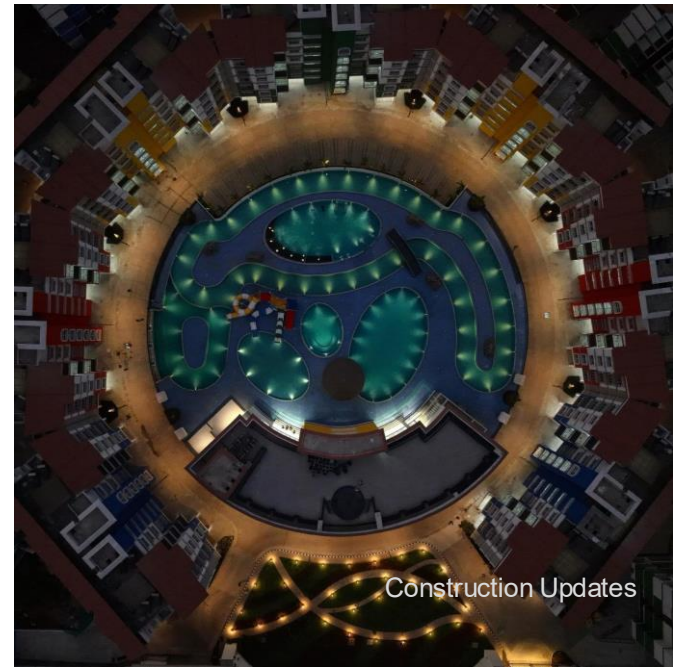

Construction Updates

CLUB HOUSE

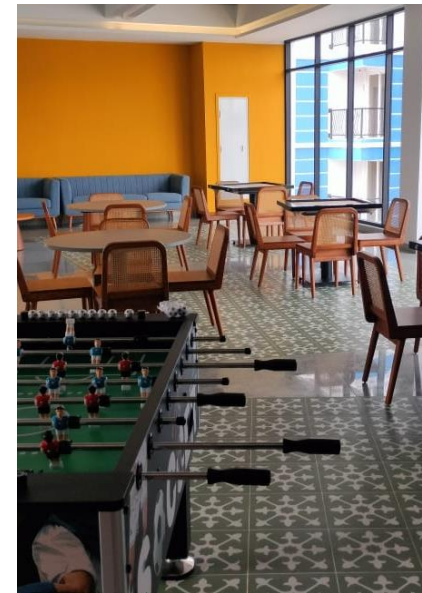


Actual site photograph

LANDSCAPE



Actual site photograph

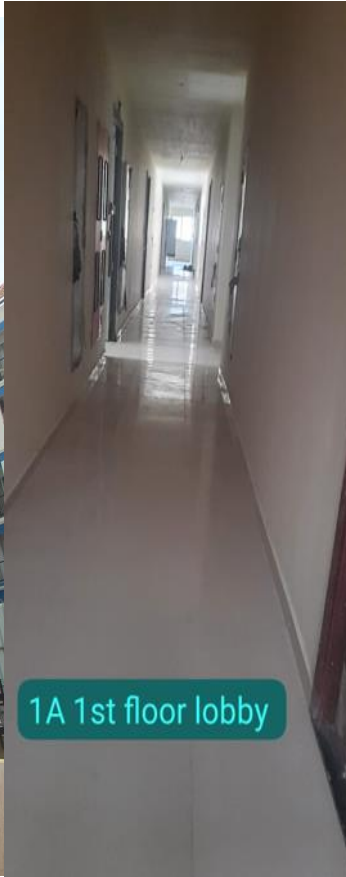

1A 1st floor lobby



1A 5th floor lobby

Row 1

TOWER STATUS

- Row 1A & 1B Customer inspection in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 1A&B terrace slab completed.
- Row 1A&B balcony railing work completion.
- Row 1A 1B staircase and granite work completed
- Row 1A&B Windows completed
- Row 1 A Sanitary & Main door completed
- Row 1 A & B External development completed



UPCOMING CONSTRUCTION MILESTONES

- Row 1B Sanitary & Main door completion

PROGRESS TIMELINE



Dec 25



Jan 26



Feb 26



Mar 26



April 26



May 26



June 26



Row 2

TOWER STATUS

- Row 2A & 2B Customer inspection in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 2A internal door fixing work completed.
- Row 2A common area tiling completed.
- Row 2A&B Windows completed
- Row 2AB Sanitary & Main door completed
- Row 2AB External development works completed



UPCOMING CONSTRUCTION MILESTONES

- Customer inspection

PROGRESS TIMELINE



Row 3



TOWER STATUS

- Row 3ABC Customer Inspection in progress
- Row 3D Snag 3 work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 3A & B flooring work completed.
- Row 3A,B,C&D external plumbing completed.
- Row 3ABC&D windows completed.
- Row 3ABCD Sanitary & Main door completed
- Row 3ABCD External development works completed



UPCOMING CONSTRUCTION MILESTONES

- Row 3ABCD Customer inspection completion

PROGRESS TIMELINE



Row 4



TOWER STATUS

- Row 4A,B Customer inspection in progress
- Row 4 C & D snag works in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 4A,B,C&D terrace slab completed.
- Row 4A,B,C & D gypsum work completed.
- Row 4A & 4B external plumbing work completed.
- Row 4ABCD Windows completed
- Row 4ABD Sanitary & Main door completed
- Row 4ABD External development work completed



UPCOMING CONSTRUCTION MILESTONES

- Row 4C Sanitary & Main door completion
- Row 4C External development completion

PROGRESS TIMELINE



Mar 26



April 26



May 26



June 26



Row 5

TOWER STATUS

- Row 5ABCD Customer inspection in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 5D completion of flooring & windows work.
- Row 5C completion of flooring & windows work.
- Row 5ABCD staircase Granite & Tander works completed
- Row 5ABCD Sanitary & Main door completed
- Row 5ABC Snag 3 completed
- Row 5ABC External development completed



UPCOMING CONSTRUCTION MILESTONES

- Row 5 ABCD Customer inspection

PROGRESS TIMELINE





Row 6

TOWER STATUS

- Row 6A B & C Customer inspection in progress
- Row 6 DE snag work in progress
- Row 6DE External development work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 6C waterproofing work completed.
- Row 6AB&C windows work completed.
- Row 6ABCDE staircase granite and tandur works completed
- Row 6ABC Main door & sanitary completed
- Row 6AB Snag 3 completed



UPCOMING CONSTRUCTION MILESTONES

- Row 6 D E Main door & Sanitary completion.
- Row 6 C D E External development completion

PROGRESS TIMELINE





Row 7

TOWER STATUS

- Row 7A B C D Internal painting work in progress
- Row 7ABCD External texture work in progress
- Row 7ABCD External development work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 7A,B,C & D waterproofing works completed.
- Row 7A sunken filing work completed.
- Row 7A 7B 7C 7D Staircase work completed
- Row 7A 7B 7C 7D Windows work completed
- Row 7A B Sanitary & Main door completed



UPCOMING CONSTRUCTION MILESTONES.

- Row 7ABCD External development work completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26

April 26

May 26

June 26



Row 8

TOWER STATUS

- Row 8BCD tiling work in progress.
- Row 8B fixing of windows work in progress
- Row 8A Internal painting work in progress
- Row 8ABCD External development work in progress



CONSTRUCTION MILESTONES ACHIEVED



- Row 8A,B,C & D Terrace slab completed.
- Row 8ABCD External plumbing work in progress
- Row 8ABCD Staircase granite and tander work completed Row 8AB Tiling completed



UPCOMING CONSTRUCTION MILESTONES

- Row 8CD completion of flooring work.
- Row 8CD completion of windows
- Row 8D staircase & Tander works completion

PROGRESS TIMELINE





Row 9

TOWER STATUS

- Row 9AB Tiling work in progress
- Row 9B External plumbing work in progress
- Row 9ABC External development in progress
- Row 9C internal painting work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 9A,B & C terrace slab completed.
- Row 9A,B & C structure work completed.
- Row 9ABC waterproofing completed
- Row 9AC External plumbing completed
- Row 9C Windows completed



UPCOMING CONSTRUCTION MILESTONES

- Row 9AB finishes works completion
- Row 9B External plumbing work completion
- Row 9AB Windows completion

PROGRESS TIMELINE



Mar 26



April 26



May 26




June 26

**External
Development/Hardscape -
WIP**



Actual site photograph

- External Development/Hardscape - WIP

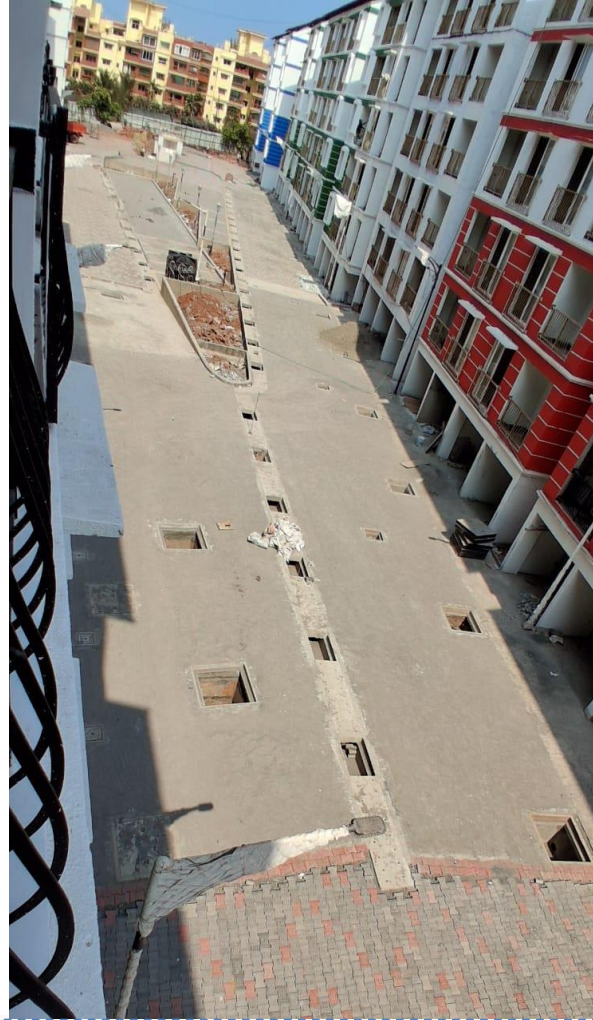

Actual site photograph

Mixed – Use Commercial



TOWER STATUS

- MUC–2nd slab for pour 1 completed.
- MUC–2nd slab for pour 2 completed.
- MUC–2nd to 3rd floor slab column pour 1 completed.
- MUC–2nd to 3rd floor column pour 2 work completed.
- MUC–2nd to 3rd pour 2 slab work completed.
- MUC–2nd to 3rd pour 3 slab work completed.
- MUC–4th floor slab pour 1 & pour 2 slab completed
- MUC–4th floor slab pour 3 completed
- MUC–4th floor to 5th floor Pour 1 column, beam & slab completed
- MUC–4th floor to 5th floor Pour 2 column, beam & slab completed
- MUC–5th floor to 6th floor Pour 1 column, beam & slab completed
- MUC–2nd, 3rd, 4th floor Block work masonry competed
- MUC–2nd 3rd & 4th floor internal plastering work in progress
- MUC - 5th floor Block work masonry in progress
- MUC–5th floor to 6th floor pour 2 slab completed
- MUC–6th floor to 7th floor pour 1 slab completed
- MUC–6th floor to 7th floor pour 2 work in progress
- MUC–7th floor to Terrace slab work in progress

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26

April 26

May 26

June 26

Contact Us



Site Office :

Provident Adora de Goa

Sy.No.198, Zuari Nagar, Vidhyanagar Colony, Chicalim, Goa –403726.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line–Project name/ unit number)

Call Us : +91- 80-67724001 / 1860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA No.: PRGO02190645 (ROW 5 & 6)

RERA Nos.: PRGO02180009 (Row 10, 11 & 12), PRGO07180544 (Row 13) PRGO07180560 (Row 14), PRGO07180561 (Row 15)
