

 **PROVIDENT**
ADORA DE GOA

Construction Updates
March 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Adora de Goa. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Adora de Goa

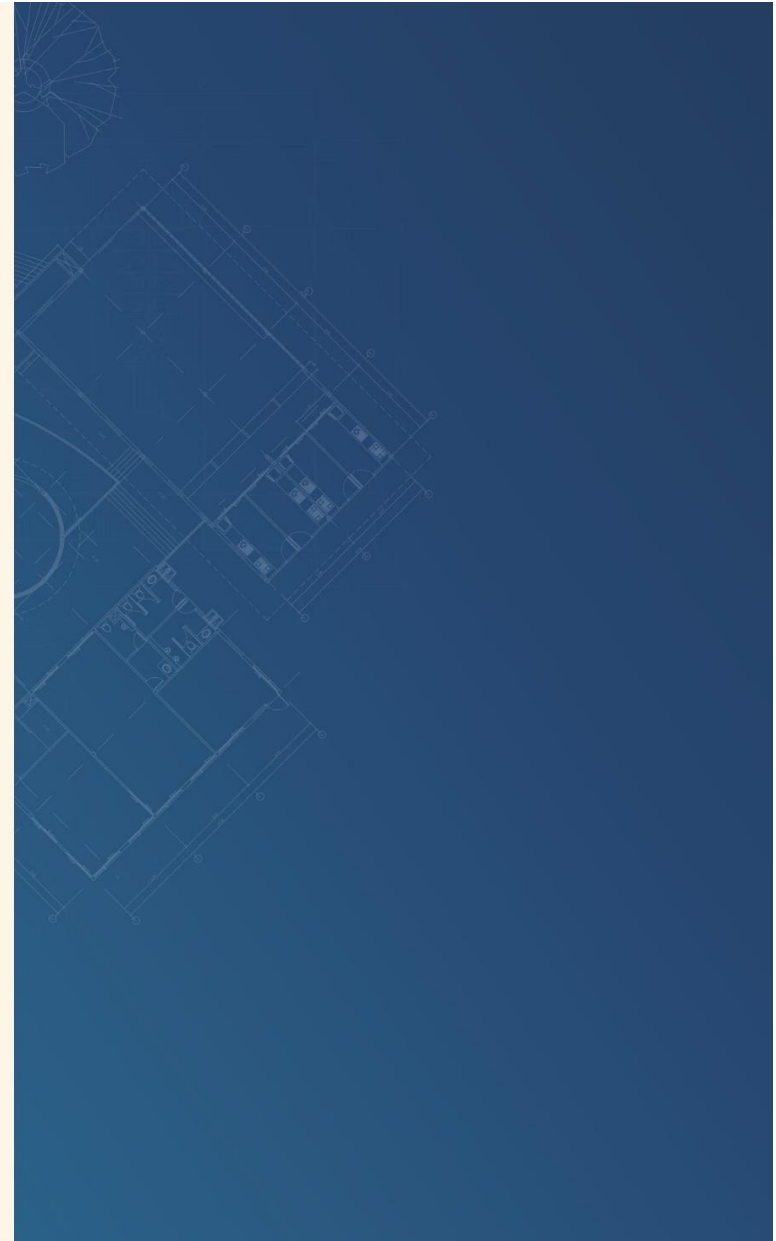



Provident Adora de Goa

Dabolim at Central Goa



Construction Updates

Overall view

BLU AREA




Actual site photograph



Construction Updates

CLUB HOUSE

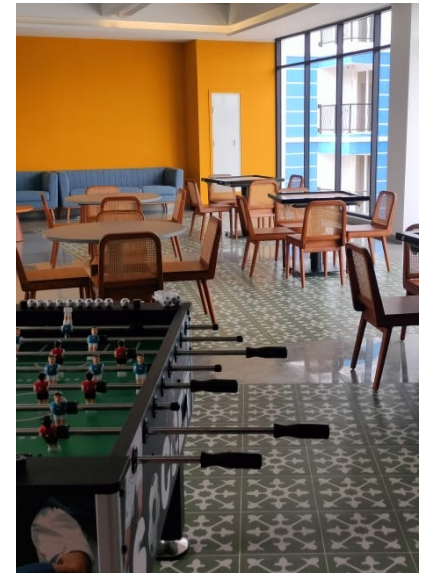

Actual site photograph

LANDSCAPE



Actual site photograph



Row 1

TOWER STATUS

- Row 1A & B snag work in progress
- Row 1A & 1B external texture works in progress
- Row 1 A Sanitary & Main door work in progress
- Row 1 A & B External development in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 1A&B terrace slab completed.
- Row 1A&B balcony railing work completion.
- Row 1A 1B staircase and granite work completed
- Row 1A&B Windows completed



UPCOMING CONSTRUCTION MILESTONES

- Row 1A & 1B Sanitary & Main door completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26



Row 2

TOWER STATUS

- Row 2A & 2B Customer inspection in progress



CONSTRUCTION MILESTONES ACHIEVED


- Row 2A internal door fixing work completed.
- Row 2A common area tiling completed.
- Row 2A&B Windows completed
- Row 2AB Sanitary & Main door completed
- Row 2AB External development works completed



UPCOMING CONSTRUCTION MILESTONES

- Customer inspection

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26



Row 3

TOWER STATUS

- Row 3A & B Customer Inspection in progress
- Row 3D Sanitary & main door in progress
- Row 3CD External development work in progress
- Row 3CD Snag 3 work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 3A & B flooring work completed.
- Row 3A,B,C&D external plumbing completed.
- Row 3ABC&D windows completed.
- Row 3ABC Sanitary & Main door completed
- Row 3AB External development works completed



UPCOMING CONSTRUCTION MILESTONES

- Row 3D Main door & Sanitary completion.
- Row 3ABCD External development completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26



Row 4

TOWER STATUS

- Row 4A,B,C & D Internal painting work in progress
- Row 4CD fixing of sanitary & main door in progress
- Row 4ABCD External development work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 4A,B,C&D terrace slab completed.
- Row 4A,B,C & D gypsum work completed.
- Row 4A & 4B external plumbing work completed.
- Row 4ABCD Windows completed
- Row 4AB Sanitary & Main door completed



UPCOMING CONSTRUCTION MILESTONES

- Row 4CD Sanitary & Main door completion
- Row 4ABCD External development completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26

Row 5



TOWER STATUS

- Row 5ABC Customer inspection in progress
- Row 5D Snag work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 5D completion of flooring & windows work.
- Row 5C completion of flooring & windows work.
- Row 5ABCD staircase Granite & Tander works completed
- Row 5ABCD Sanitary & Main door completed
- Row 5ABC Snag 3 completed
- Row 5ABC External development completed



UPCOMING CONSTRUCTION MILESTONES

- Row 5 ABCD Customer inspection

PROGRESS TIMELINE



Row 6



TOWER STATUS

- Row 6A & B Customer inspection in progress
- Row 6C snag work in progress
- Row 6 DE main door & sanitary fixing in progress
- Row 6CDE External development work in progress



CONSTRUCTION MILESTONES ACHIEVED


- Row 6C waterproofing work completed.
- Row 6AB&C windows work completed.
- Row 6ABCDE staircase granite and tandur works completed
- Row 6ABC Main door & sanitary completed
- Row 6AB Snag 3 completed



UPCOMING CONSTRUCTION MILESTONES

- Row 6 D E Main door & Sanitary completion.
- Row 6 C D E External development completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26

Row 7



TOWER STATUS

- Row 7A B C D Internal painting work in progress
- Row 7A B C D Sanitary & Main door fixing in progress
- Row 7ABCD External texture work in progress



CONSTRUCTION MILESTONES ACHIEVED

- Row 7A,B,C & D waterproofing works completed.
- Row 7A sunken filing work completed.
- Row 7A 7B 7C 7D Staircase work completed
- Row 7A 7B 7C 7D Windows work completed



UPCOMING CONSTRUCTION MILESTONES.

- Row 7ABCD Sanitary & Main door completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26



Row 8

TOWER STATUS

- Row 8ABCD tiling work in progress.
- Row 8AB fixing of windows work in progress
- Row 8CD staircase & Tander work in progress



CONSTRUCTION MILESTONES ACHIEVED


- Row 8A,B,C & D Terrace slab completed.
- Row 8ABCD External plumbing work in progress



UPCOMING CONSTRUCTION MILESTONES

- Row 8ABCD completion of flooring work.
- Row 8ABCD completion of windows
- Row 8CD staircase & Tander works completion

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26



Row 9

TOWER STATUS

- Row 9ABC Tiling work in progress
- Row 9AB External plumbing work in progress



CONSTRUCTION MILESTONES ACHIEVED


- Row 9A,B & C terrace slab completed.
- Row 9A,B & C structure work completed.
- Row 9ABC waterproofing completed



UPCOMING CONSTRUCTION MILESTONES

- Row 9ABC finishes works completion
- Row 9ABC External plumbing work completion
- Row 9ABC Windows completion

PROGRESS TIMELINE

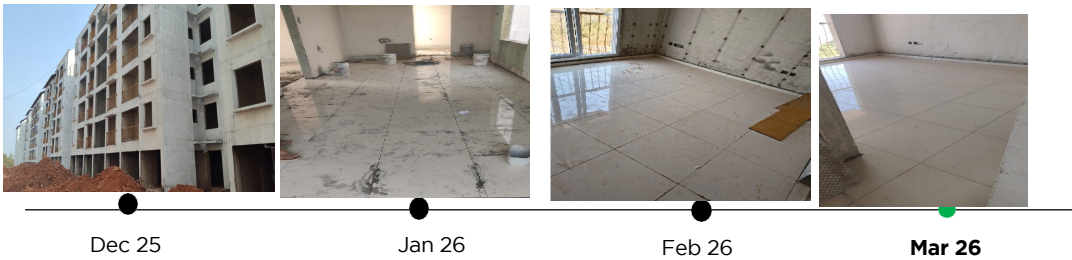


**External
Development/Hardscape -
WIP**



Actual site photograph

- External Development/Hardscape - WIP

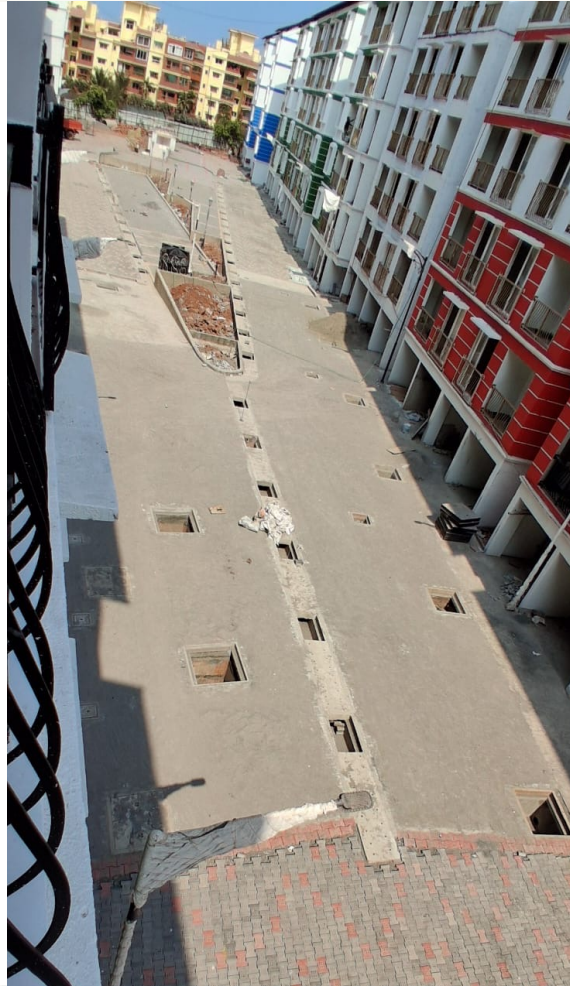

Actual site photograph

Mixed - Use Commercial



TOWER STATUS

- MUC - 2nd slab for pour 1 completed.
- MUC - 2nd slab for pour 2 completed.
- MUC - 2nd to 3rd floor slab column pour 1 completed.
- MUC - 2nd to 3rd floor column pour 2 work completed.
- MUC - 2nd to 3rd pour 2 slab work completed.
- MUC - 2nd to 3rd pour 3 slab work completed.
- MUC - 4th floor slab pour 1 & pour 2 slab completed
- MUC - 4th floor slab pour 3 completed
- MUC - 4th floor to 5th floor Pour 1 column, beam & slab completed
- MUC - 4th floor to 5th floor Pour 2 column, beam & slab completed
- MUC - 5th floor to 6th floor Pour 1 column, beam & slab completed
- MUC - 2nd , 3rd & 4th floor Block work masonry in progress
- MUC - 5th floor to 6th floor pour 2 work in progress
- MUC - 6th floor to 7th floor pour 1 work in progress

PROGRESS TIMELINE



Dec 25

Jan 26

Feb 26

Mar 26

Contact Us



Site Office :

Provident Adora de Goa

Sy.No.198, Zuari Nagar, Vidhyanagar Colony, Chicalim, Goa - 403726.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-4455544

Email : crm@providenthousing.com (Subject line - Project name/ unit number)

Call Us : +91- 80-67724001 / 1860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA No.: PRGO02190645 (ROW 5 & 6)

RERA Nos.: PRGO02180009 (Row 11 & 12), PRGO07180544 (Row 13)

PRGO07180560 (Row 14), PRGO07180561 (Row 15)
