



## Construction Updates

November 2025



*Dear Esteemed Customer,*


*Greetings from Provident*

*It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Adora de Goa. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.*

*We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.*

*We are grateful for your kind cooperation.*

*Team Provident Adora de Goa*

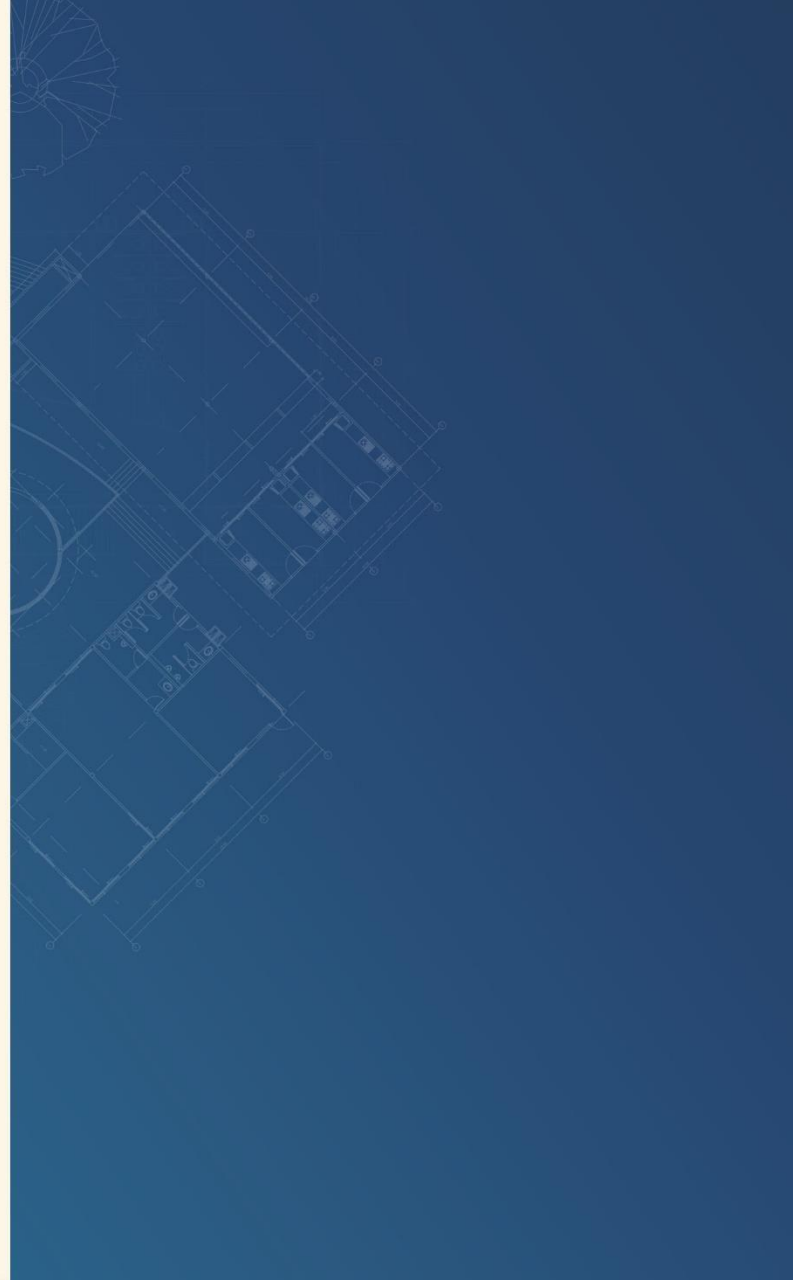



# Provident Adora de Goa

Dabolim at Central Goa




## Construction Updates

Overall view

# BLU AREA




Actual site photograph

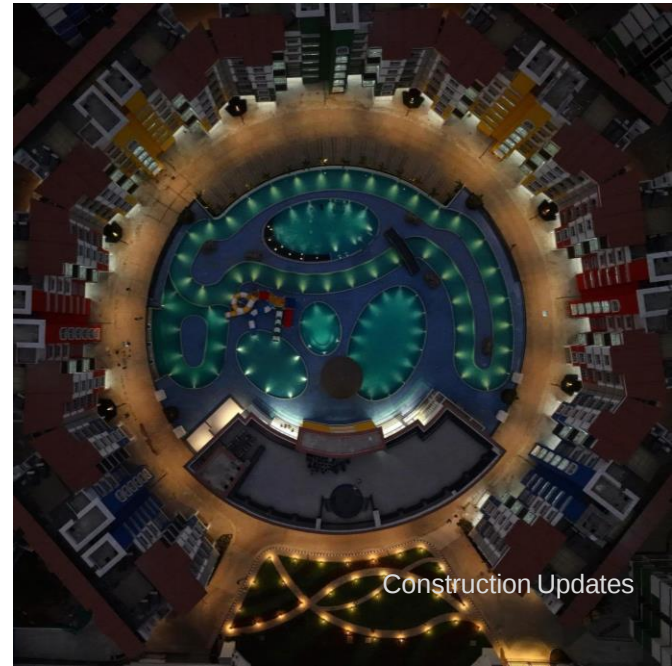

Construction Updates

# CLUB HOUSE

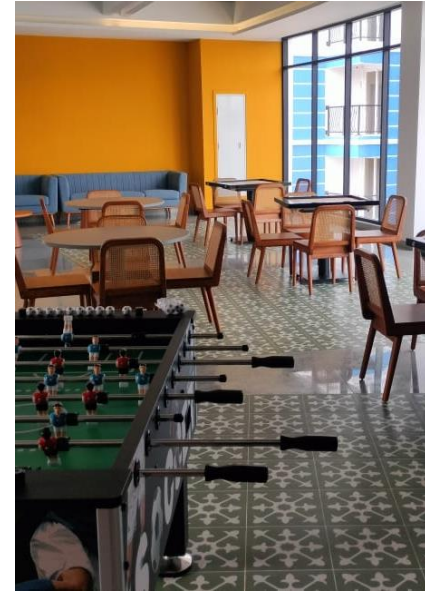

Actual site photograph

# LANDSCAPE



Actual site photograph

# Row 1



## TOWER STATUS

- Row 1A finishing work in progress.
- Row 1B finishing work in progress.
- Row 1A & 1B external texture works in progress
- Row 1A & B window fixing work in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 1A&B terrace slab completed.
- Row 1A&B balcony railing work completion.
- Row 1A 1B staircase



## UPCOMING CONSTRUCTION MILESTONES

- Row 1A&B Windows fixing.
- Row 1A & 1B Sanitary & Main door completion

## PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

# Row 2



## TOWER STATUS

- Row 2A & 2B External texture works in progress.
- 2A& 2B Internal painting work in progress.
- 2B Internal door fixing in progress.
- Row 2AB Sanitary and main door work in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 2A internal door fixing work completed.
- Row 2A common area tiling completed.
- Row 2A&B Windows completed



## UPCOMING CONSTRUCTION MILESTONES

- Row 2 A & B Sanitary & Main door completion

## PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

# Row 3



## TOWER STATUS

- Row 3 ABCD External texture works in progress
- Row 3C & 3D internal doors fixing in progress
- Row 3A & B Internal painting work in progress
- Row 3A Sanitary & main door in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 3A & B flooring work completed.
- Row 3A,B,C&D external plumbing completed.
- Row 3ABC&D windows completed.



## UPCOMING CONSTRUCTION MILESTONES

- Row 3ABCD Main door & Sanitary completion.

## PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

# Row 4



## TOWER STATUS

- Row 4A,B Internal painting work in progress
- Row 4 C & D floor tiling work in progress.
- Row 4ABCD fixing of windows in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 4A,B,C&D terrace slab completed.
- Row 4A,B,C & D gypsum work completed.
- Row 4A & 4B external plumbing work completed.



## UPCOMING CONSTRUCTION MILESTONES

- Row 4A,B,C & D Windows completion
- Row 4BCD Staircase granite and tandur works completion

## PROGRESS TIMELINE



Aug 25



Sep 25



Oct 25



Nov 25

# Row 5



## TOWER STATUS

- Row 5CD Main Door Fixing in progress.
- Row 5 C & D Sanitary fixing in progress.
- Row 5ABCD Internal painting in progress
- Row 5ABCD external texture works in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 5A,B,&C Vitrified flooring completed.
- Row 5D completion of flooring & windows work.
- Row 5C completion of flooring & windows work.
- Row 5ABCD staircase Granite & Tander works completed
- Row 5AB Sanitary & UP COMING completed



## UPCOMING CONSTRUCTION MILESTONES

- Row 5ABCD Main door & Sanitary fixing.

## PROGRESS TIMELINE



Aug 25



Sep 25



Oct 25



Nov 25

# Row 6



## TOWER STATUS

- Row 6AB Internal painting work in progress
- Row 6ABCDE External texture work in progress.
- Row 6 B main door & sanitary fixing in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 6A,B,C&D terrace slab completed.
- Row 6C waterproofing work completed.
- Row 6AB&C windows work completed.
- Row 6ABCDE staircase granite and tandur works completed
- Row 6A Main door & sanitary completed



## UPCOMING CONSTRUCTION MILESTONES

- Row 6 A B C D E Main door & Sanitary completion.

## PROGRESS TIMELINE



Actual site photograph

# Row 7



## TOWER STATUS

- Row 7A , 7B , 7C, 7D floor tile work in progress.
- Row 7A Staircase Granite & Tandur work in progress
- Row 7A fixing of windows in progress
- Row 7D staircase Tandur & Granite work in progress
- Row 7A Internal painting work in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 7A,B,C&D terrace slab completed.
- Row 7A,B,C & D waterproofing works completed.
- Row 7A sunken filing work completed.



## UPCOMING CONSTRUCTION MILESTONES

- Row 7ABCD windows completion.
- Row 7ABCD staircase granite & tandur works completion

## PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

# Row 8



## TOWER STATUS

Row 8ABCD tiling work in progress.  
Row 8D External plumbing work in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 8A,B,C & D Terrace slab completed.



## UPCOMING CONSTRUCTION MILESTONES

- Row 8ABCD completion of flooring work.
- Row 8ABCD completion of windows

## PROGRESS TIMELINE



Actual site photograph

# Row 9



## TOWER STATUS

- Row 9A,B&C above terrace works are in progress.
- Row 9C External plumbing work in progress



## CONSTRUCTION MILESTONES ACHIEVED

- Row 9A,B & C terrace slab completed.
- Row 9A,B & C structure work completed.
- Row 9ABC waterproofing completed



## UPCOMING CONSTRUCTION MILESTONES

- Row 9A finishes work to complete

## PROGRESS TIMELINE



Actual site photograph


# External Development/Hardscape - WIP



Actual site photograph



# External Development/Hardscape - WIP

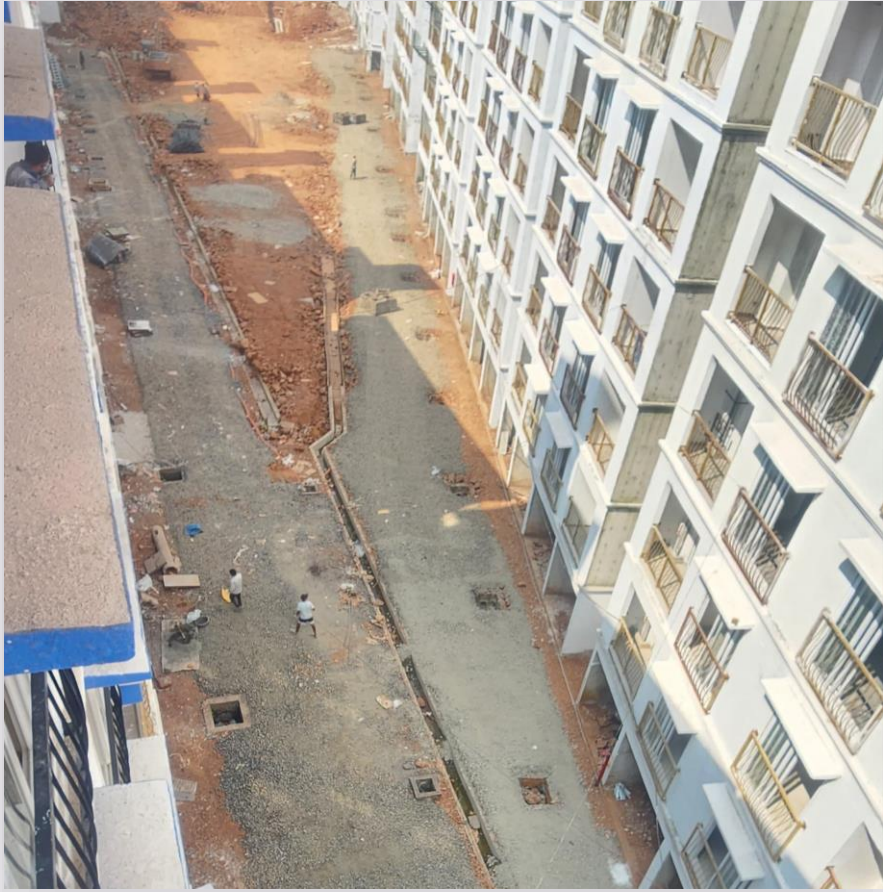

Actual site photograph

# Mixed - Use Commercial



## TOWER STATUS

- MUC - 2<sup>nd</sup> slab for pour 1 completed.
- MUC - 2<sup>nd</sup> slab for pour 2 completed.
- MUC - 2<sup>nd</sup> to 3<sup>rd</sup> floor slab column pour 1 completed.
- MUC - 2<sup>nd</sup> to 3<sup>rd</sup> floor column pour 2 work completed.
- MUC - 2<sup>nd</sup> to 3<sup>rd</sup> pour 2 slab work completed.
- MUC - 2<sup>nd</sup> to 3<sup>rd</sup> pour 3 slab work completed.
- MUC - 4<sup>th</sup> floor slab pour 1 & pour 2 slab completed
- MUC - 4<sup>th</sup> floor slab pour 3 completed
- MUC - 4<sup>th</sup> floor to 5<sup>th</sup> floor Pour 1 column, beam & slab completed
- MUC - 4<sup>th</sup> floor to 5<sup>th</sup> floor Pour 2 column, beam & slab work in progress

## PROGRESS TIMELINE



Aug 25



Sep 25



Oct 25



Nov  
25

Actual site photograph

Construction Updates

# Contact Us



## Site Office :

Provident Adora de Goa

Sy.No.198, Zuari Nagar, Vidhyanagar Colony, Chicalim, Goa – 403726.

## Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

**Email :** [crm@providenthousing.com](mailto:crm@providenthousing.com) (Subject line – Project name/ unit number)

**Call Us :** +91- 80-67724001 / 1860 208 0000

**Web :** [www.providenthousing.com](http://www.providenthousing.com)

## RERA Registration Number :

RERA No.: PRGO02190645 (ROW 5 & 6)

RERA Nos.: PRGO02180009 (Row 10, 11 & 12), PRGO07180544 (Row 13)

PRGO07180560 (Row 14), PRGO07180561 (Row 15)
