



Construction Updates

November 2025



Dear Esteemed Customer,

Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Winworth. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Winworth





Provident Winworth

Edappally, Kochi



Construction Updates

Overall view

Tower 1



PROGRESS TIMELINE



Sep 25

Oct 25

Nov 25

Actual site photograph

TOWER STATUS

- Internal Block Work & Wall plastering completed up to the 21st floor.
- Tiling work completed at the 21st floor.
- Plumbing sanitary fixing started.
- FPS sprinkler works completed at 21st floor.
- External plastering works 100% completed
- Putty works in progress at 21st floor.
- Staircase Handrails completed.
- Inside flats wiring completed up to 21st floor.



CONSTRUCTION MILESTONES ACHIEVED

- Structural works completed .
- Blockwork completed up to terrace level.
- Tiling work completed up to 21st Floor.
- Primer coat inside flats completed up to 14th floor
- .UPVC work completed up to 20th floor.
- Door frame fixing works completed from 3rd to 10th floor
- External painting works commenced on three sides.
- .IPS flooring work at 2nd floor parking area completed
- Terrace waterproofing 100% completed. Clay tiling started
- Lift 1&2 -cabin erected.



UPCOMING CONSTRUCTION MILESTONES

- Completion of doorframe fixing at 12th floor

Construction Updates

Tower 2



PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

TOWER STATUS

- Internal Block Work & Wall plastering completed up to the 21st floor.
- Tiling work completed at the 21st floor.
- Plumbing concealed works inside the flat completed till 21st floor.
- FPS sprinkler works in progress at 21st floor.
- External plastering works completed .
- Putty works in progress at 21st floor.
- Staircase Handrails completed.
- IPS Flooring second floor Parking 80% completed
- Inside flats wiring completed up to 20th floor
- UPVC windows up to 19th floor fixing completed



CONSTRUCTION MILESTONES ACHIEVED

- Structural works completed
- Block Work up to roof top completed.
- Tiling work at 21st floor completed.
- Primer coat work completed till 9th floor inside flats.
- UPVC work in progress at 20th floor
- External painting works commenced.
- IPS flooring work at second floor commenced.
- Handrails fixing of balcony 98%.
- High level fire and plumbing works at second floor car parking header lines completed.
- Door fixing up to 6th floor completed.
- Lift (4) cladding up to 14th floor.




UPCOMING CONSTRUCTION MILESTONES

- Completion of Door frames fixing inside flats up to 6th floor & 7th floor

Construction Updates

Tower 3

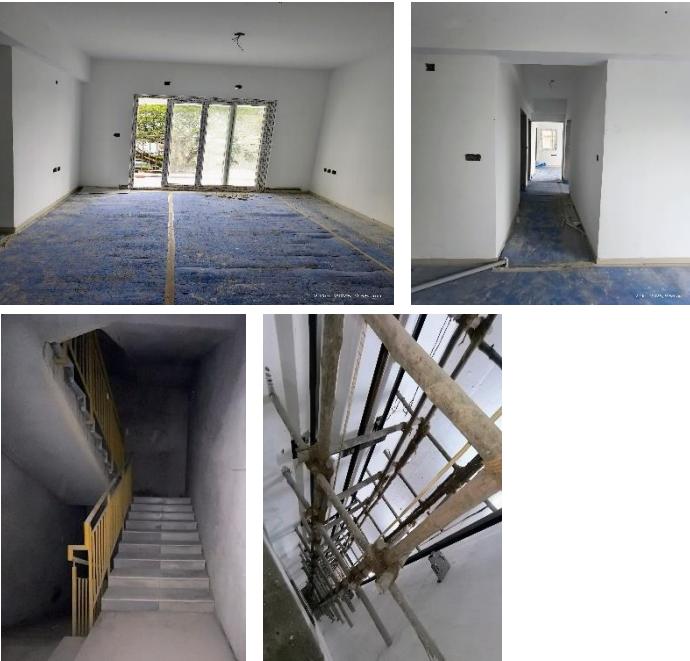

TOWER STATUS

- Internal Block work completed up to 21st.
- Internal Plastering in progress at 20th floor.
- Plumbing concealed work completed till 19th floor.
- Tiling work in progress at 19th floor.
- UPVC windows works in progress at 7th floor.
- External painting started.
- Wiring at Flats completed up to 4th floor.
- Balcony and stair hand rails 80% completed



CONSTRUCTION MILESTONES ACHIEVED

- Structural works completed up to the roof
- Tiling work commenced at 19th floor.
- IPS flooring 80% completed at first floor.
- Lift erecting work commenced



UPCOMING CONSTRUCTION MILESTONES

- Commencement of Tiling works 19th and 20th Floor.

PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

Construction Updates

Tower 4



PROGRESS TIMELINE



Aug 25

Sep 25

Oct 25

Nov 25

Actual site photograph

TOWER STATUS

- Internal Block work completed at 12th floor.
- Internal plastering completed at 10th floor
- Internal Plumbing work progressing at 10th floor.
- Electrical chasing work progressing at 11th floor.
- External plastering works progressing at 12th floor level.
- Tiling works progress at 9th floor.
- Stair& balcony handrail works in progress
- External painting progressing.



CONSTRUCTION MILESTONES ACHIEVED

- Structural works up to roof Level completed.
- Tiling works commenced at 9th floor



UPCOMING CONSTRUCTION MILESTONES

- Commencement of Tile works at 10th floor.

Construction Updates

Clubhouse



Contact Us



Site Office :

Provident Winworth

No-41/199A, Padivattom, NH-47 Byepass,
Edappally, Kochi, Kerala - 682 024.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line - Project name/ unit number)

Call Us : +91 - 80-67724001 / 1860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA No.: K-RERA/PRJ/ERN/020/2022
