

PROVIDENT DEANSGATE

Construction Updates

August 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Deansgate

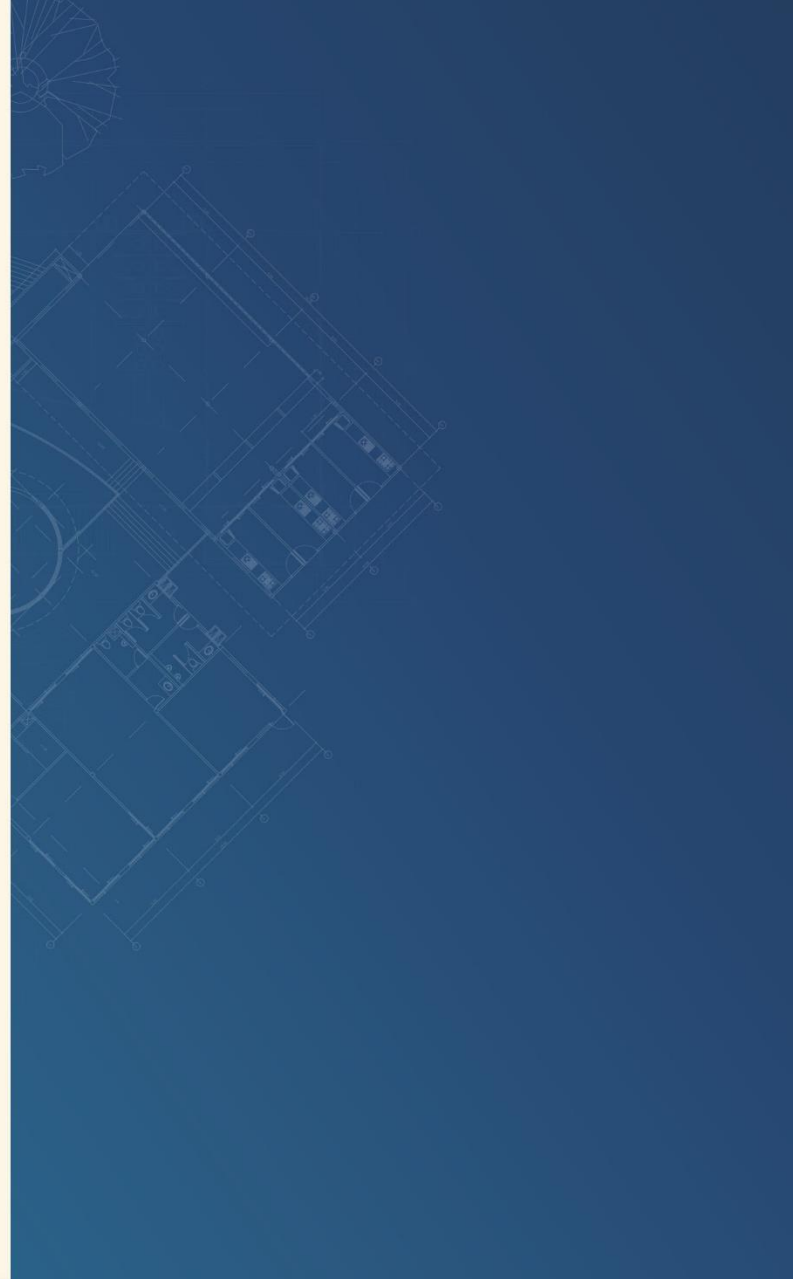



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER D (D1/N07)



Actual site photograph

CLUSTER D STATUS

- Handed over to Facility Team. Final Handing over completed.



MILESTONES
ACHIEVED



UPCOMING
MILESTONES

PROGRESS TIMELINE



July'26

CLUSTER D (D4/N04 to D2/N06)



Actual site photograph

CLUSTER D STATUS

- N4 –1st coat paint work completed.. Lift work completed. Electrical wire pulling work in progress.
- N5 –Lift work completed. Ceiling First coat paint work completed. Wall primer completed. Wire pulling work need to start.
- N6 –Lift work completed. Ceiling First coat paint work completed. Wall primer completed. Wire pulling work need to start.



MILESTONES ACHIEVED

UPCOMING MILESTONES

PROGRESS TIMELINE



July'26

CLUSTER D (D7/N01 TO D5/N03)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER D STATUS

- N1-.Installation of Door work In progress.. POP Work in progress. Electrical wire pulling work in progress. Lift work completed.
- N2- Lift work completed. POP Work completed. Electrical wire pulling work in progress.
- N3-Lift work completed. Primer sanding work in progress. Electrical wire pulling work need to start. POP Work completed.



MILESTONES ACHIEVED

- N2/D6- Installation of Door Completed.



UPCOMING MILESTONES

- N1/D7- Installation of Door to be complete.

Cluster C (C4/N11 to C1/N14)



Actual site photograph

PROGRESS TIMELINE



July'26

Cluster C STATUS

- N11 – Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Snagging work in progress.
- N12- Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Snagging work in progress.
- N-13- Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Deep cleaning work in progress.
- N14- Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Deep cleaning work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

Cluster C (C7/N8 to C5/N10)



Actual site photograph

PROGRESS TIMELINE



July'26

Cluster C STATUS

- N8- Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Snagging work in progress.
- N9 –Lift work completed & 2nd coat paint work completed. Electrical wire pulling work completed .Snagging work in progress.
- N10- Lift work completed & 2nd coat paint work in progress.. Electrical wire pulling work completed .Snagging work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

CLUSTER C (C8/S09 to C11/S12)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER C STATUS

S9 –FF Flooring work in progress. Lift Internal Wall plastering work in progress. SF Waterproofing work completed.GF Flooring work completed.2nd cot putty work in progress.

S10- Lift inside Internal plastering work in progress .GF & FF Floor & toilet screed completed. SF screed work need to start.1st coat putty work completed.

- S11- Backside External Cladding work in progress.GF Flooring work completed. Lift inside Internal plastering work in progress.GF & FF Floor screed &toilet screed work completed. SF Screed work need to start.
- S12-External Cladding work in progress. Backside External plastering work completed. Internal Wall plastering work in completed.1st coat putty work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- 1. S9/C8 =Installation of External windows & Completion of Flooring need to be complete.
- 2. S10/C9 =Installation of External windows & Completion of Flooring need to be complete.

CLUSTER C (C12/S13 to C14/S15)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER C STATUS

- S13 - Backside External plastering work completed. Backside External Cladding work need to start. GF Flooring work completed. FF Flooring work need to start. GF Staircase Handrailing completed. 1st coat putty work completed.
- S14 - Backside External plastering work completed. Front side External Cladding work completed. GF Flooring work completed. FF Flooring work need to start. 1st coat putty work completed. GF Staircase railing work completed.
- S15- Backside External plastering work completed. Backside External Cladding work need to start. GF Flooring work need to start. GF Staircase Handrailing completed. 1st coat putty work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- S13-Completion of Flooring need to be complete.
- S14-Completion of Flooring need to be complete.
- S15-Completion of Flooring need to be complete.

CLUSTER A (A10/S20 to A12/S22)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER A STATUS

- S20- FF floor screed completed. Backside External cladding work completed . Flooring work need to start. Lift work in progress.
- S21- Backside External cladding work in progress. FF Floor screed completed Flooring work need to start
- S22- Backside External cladding work in progress. FF Floor screed completed Flooring work need to start



MILESTONES ACHIEVED



UPCOMING MILESTONES

CLUSTER A (A06/S16 to A09/S19)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER A STATUS

- S16-External cladding work completed. SF 1ST Coat putty work completed. Lift work in progress .SF & FF Flooring work in progress.
- S17 -External cladding work completed. FF & SF 1ST Coat putty work completed. Lift work in progress. SF & FF Flooring work need to start.
- S18 - Toilet screed work completed. FF Floor Screed work completed. 1st Coat putty work completed. Flooring work need to start.
- S19- Toilet screed work completed. FF Floor Screed work completed. 1st Coat putty work completed. Flooring work need to start.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- S16-Flooring work need to complete.
- S17-Flooring work need to complete.
- S18-Flooring work need to complete.

CLUSTER A (A05/N15 to A01/N19)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER A STATUS

- N15- 1st coat putty work completed. "C" Channel installing work completed. External cladding work and flooring work need to start. Toilet waterproofing work in progress.
- N16-1st coat putty work completed. "C" Channel installing work completed. External cladding work and flooring work need to start. Toilet waterproofing work in progress.
- N17-1st coat putty work completed. "C" Channel installing work completed. Toilet waterproofing work in progress. Flooring work need to start.
- N18- 1st coat putty work completed. "C" Channel installing work completed. Toilet waterproofing work completed Flooring work need to start.
- N19- 1st coat putty work completed. "C" Channel installing work completed. Toilet waterproofing work completed. Flooring work need to start.



MILESTONES ACHIEVED



UPCOMING MILESTONES

CLUSTER D (D12/S05 to D15/S08)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER D STATUS

- S5-UPVC window installation work completed.2nd coat putty work in progress. Backside External cladding work need to start. Door installation work need to start. Lift work in progress.
- S6- UPVC window installation work completed.2nd coat putty work in progress. Backside External cladding work need to start. Door installation work need to start. Lift work in progress.
- S7- Completion of Flooring completed. Backside External cladding work in progress. GF & FF Staircase Flooring and Granite wok completed. Lift installation work in progress.
- S8- Completion of Flooring completed. Backside External cladding completed. GF & FF Staircase Flooring and Granite wok completed. Lift installation work in progress.



MILESTONES ACHIEVED

- S05/D12–Installation of External windows completed.
- S06/D13–Installation of External windows completed.
- S07/D14–Installation of External Windows & Completion of Floor tiling completed.
- S08/D15–Installation of External Windows & Completion of Floor tiling completed.



UPCOMING MILESTONES

- S05/D12 -Installation of door need to be complete.
- S06/D13 –Installation of Door need to be complete.
- S07/D14 -Installation of Door need to be complete.
- S08/D15 -Installation of Door need to be complete.

CLUSTER D (D08/S01 to D11/S04)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER D STATUS

- S1- Installation of external windows & Doors completed. 2nd coat putty work completed & Backside External cladding work need to start. snag work in progress.
- S2-Installation of external windows & Doors completed. 2nd coat putty work completed & Backside External cladding work need to start. snag work in progress.
- S3-Installation of external windows completed & installation of Door work in progress. 2nd Coat Putty work completed.
- S4- Installation of external windows completed & installation of Door work in progress. 2nd Coat Putty work completed.



MILESTONES ACHIEVED

- S01/D8 –Installation of Door completed.
- S03/D10 –Installation of External Windows completed.
- S04/D11–Installation of External Windows completed.



UPCOMING MILESTONES

- S02/D9-Installation of Door need to be complete .
- S03/D10-Installation of Door need to be complete .
- S04/D11 -Installation of Door need to be complete .

CLUSTER B (B04/E05 to B02/E07)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER B STATUS

- E5- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed.
- E6- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed .
- E7- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed. Duplex staircase flooring work completed. installation of window work need to start.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- B02/E07 –Installation of External Windows need to be done.
- B03/E06 –Installation of External Windows & completion of flooring need to be done.

CLUSTER B (B08/E01 to B05/E04)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER B STATUS

- E1-Internal Flooring work completed. Backside External plastering work completed. Backside External Cladding work in progress. Lift installation work in progress. "C" Channel work completed.
- E2- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed
- E3- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed
- E4- Internal Flooring work completed. Backside External plastering work completed. Lift installation work in progress. "C" Channel work completed



MILESTONES ACHIEVED

- E1- Completion of Flooring completed.
- E2- Completion of Flooring completed.
- E3- Completion of Flooring completed.
- E4- Completion of Flooring completed.



UPCOMING MILESTONES

- E1 – Installation of External Windows need to be done.
- E2 – Installation of External Windows need to be done.
- E3 – Installation of External Windows need to be done.
- E4 – Installation of External Windows need to be done.

CLUSTER B (W1/B1)



Actual site photograph

CLUSTER B STATUS

- W1–Internal plastering work completed
.External plastering work completed. Toilet plumbing work in progress. Putty work in progress. Frontside External cladding work completed.



MILESTONES ACHIEVED



UPCOMING MILESTONES

PROGRESS TIMELINE



July'26

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/041123/006373
