

PROVIDENT DEANSGATE

Construction Updates

August 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Deansgate

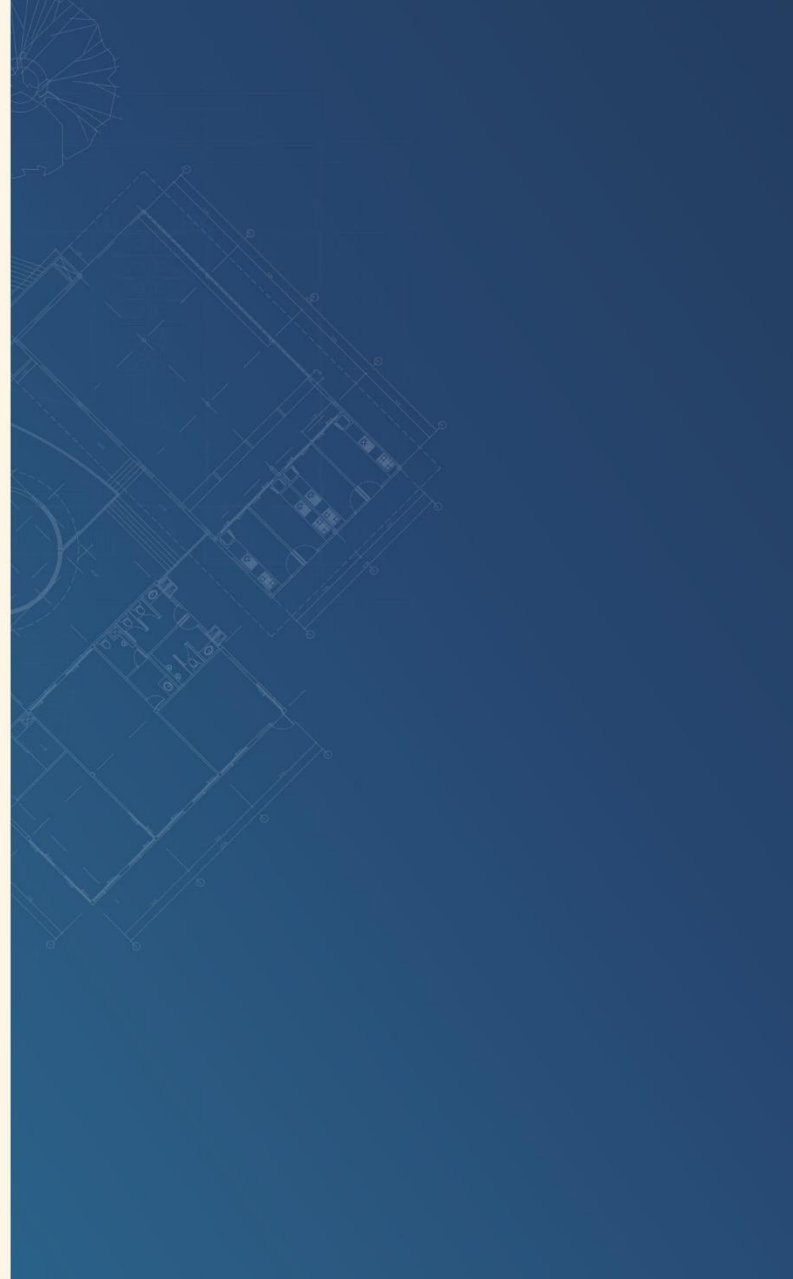



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER F (F14/S23 TO F08/S29)



Actual site photograph

PROGRESS TIMELINE



July'26



MILESTONES ACHIEVED

CLUSTER F STATUS

- S23-All work completed.
- S24-UPVC Window fixing completed & primer Work in progress.
- S25-Window fixing work need to start.
- S26- SF plastering & screed completed, Flooring work need to start. Backside External plastering work completed.
- S27-SF Internal plastering work completed & screed work need to start. GF putty work completed. Backside External plastering work completed.
- S28-FF Plastering work completed & SF Electrical work in progress. Backside External plastering work completed.
- S29-FF Plastering work completed & SF Electrical work completed . Plastering work need to start. Backside External plastering work completed.



UPCOMING MILESTONES

CLUSTER H (H01/N27 TO H06/N32)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER H STATUS

- N27- TF Slab completed. FF Plastering work completed. SF block work need to start.
- N28- TF Slab completed. FF Plastering work completed. SF block work need to start.
- N29-TF Slab work in progress. FF Plastering work completed.
- N30-TF Slab completed. FF Plastering work completed. SF block work need to start
- N31-TF Slab completed. FF Plastering work need to start. SF block work in progress.
- N32-TF Slab completed. FF Plastering work need to start. SF block work in progress.



MILESTONES ACHIEVED

- N28/H2- TF Floor slab work completed.
- N30/H4- TF Floor slab work completed.



UPCOMING MILESTONES

- N29/H3- 3rd Floor slab work to be complete.

CLUSTER H (H12/S30 TO H07/S35)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER H STATUS

- S30-Construction of Block work completed. FF & GF plastering work completed. SF plastering work in progress.
- S31-SF Block work in progress. FF block work completed & plastering work completed.
- S32-FF Block work & plastering work completed. SF Block work need to start. GF plastering work completed.
- S33-FF Block work completed. FF Plastering work in progress. SF Block work need to start. GF plastering work completed.
- S34- TF Slab shuttering work in progress. FF block work & plastering work completed. GF Block work completed & plastering work completed
- S35-TF Slab work need to start . FF block work need to start. GF Block work completed & Plastering work need to start.



MILESTONES ACHIEVED

- S30/H12- Construction of wall- completed.

UPCOMING MILESTONES

- S34/H8-3rd Floor slab work to be Complete
- S35/H7-3rd Floor slab work to be Complete
- S31/H13- Construction of wall to be complete

CLUSTER J (J17/N49 TO J20/N52)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER J STATUS

- N49- Construction of Block work completed. GF , FF & SF Plastering work completed. Frontside External plastering work in progress.
- N50- Construction of Block work completed. GF , FF & SF Plastering work completed. Frontside External plastering work in progress.
- N51-Construction of Block work completed. GF,FF & SF plastering work completed.
- N52-Construction of Block work completed. GF,FF & SF plastering work completed.



MILESTONES ACHIEVED

- N52- Construction of Block work Completed.



UPCOMING MILESTONES

CLUSTER J (J10/N42 TO J13/N45)



Actual site photograph

CLUSTER J STATUS

- N-42 –Plinth beam completed .Grade slab work in progress.
- N43- Plinth beam completed .Grade slab completed.GF to FF Column completed.
- N-44 – Plinth beam completed & Grade slab work Completed. GF to FF Columns completed.
- N-45-1st & 2nd & 3rd Floor slab completed.GF Block work in progress.



MILESTONES ACHIEVED

- N-45 – TF Slab completed.



UPCOMING MILESTONES

PROGRESS TIMELINE



July'26

CLUSTER J (J14/N46 TO J16/N48)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER J STATUS

- N-46 –TF Slab work completed.GF Block work completed.GF plastering work in progress. FF block work need to start.
- N-47 –TF Slab completed. GF Block work completed. FF Block work in progress. GF plastering work in progress.
- N-48-TF Slab completed. FF & GF Block work completed. SF Block work in progress. GF plastering work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

CLUSTER J (J01/N33 TO J05/N37)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER J STATUS

- N33-TF Slab shuttering & reinforcement work in progress. GF Block work completed & GF plastering work completed.
- N34- SF Slab shuttering work in progress. GF Block work completed & GF plastering work completed.
- N35- SF slab completed. TF Column work in progress. GF Block work completed. GF Plastering work completed.
- N36- SF Slab shuttering work need to start. GF Block work completed. GF Plastering work need to start.
- N37- FF to SF Columns completed. SF slab shuttering work need to start. GF Block work need to start.



MILESTONES ACHIEVED

- N-35- SF Slab work completed.



UPCOMING MILESTONES

- N36/J4-2nd Floor slab to be complete.
- N37/J-2nd Floor slab to be complete.

CLUSTER J (J06/N38 TO J09/N41)



Actual site photograph

PROGRESS TIMELINE



July26

CLUSTER J STATUS

- N38- SF Columns work completed. SF Slab work need to start.GF Block work in progress.
- N39- SF Columns work in progress.GF Block work in progress.
- N40- Plinth beam reinforcement completed & shuttering work in progress.
- N41-Plinth beam reinforcement completed & shuttering work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N40/J8- Plinth beam need to be Complete.
- N41/J9- Plinth beam need to be Complete.

CLUSTER F (F1/N20 TO F7/N26)



Actual site photograph

PROGRESS TIMELINE



July'26

CLUSTER J STATUS

- N20- TF Slab completed.GF block work completed.GF electrical work in progress.
- N21-TF Slab completed.GF block work completed.GF electrical work in progress..
- N22- TF Slab shuttering work in progress.. GF block work completed.GF electrical work in progress.
- N23-2nd Floor slab completed. SF to TF Columns work in progress. TF Slab work need to be start.
- N24- -2nd Floor slab completed. SF to TF Columns work in progress.
- N25-FF Slab work completed. SF Slab shuttering work in progress.
- N26-FF Slab shuttering work completed. FF to SF Columns work in progress.



MILESTONES ACHIEVED

- N20/F01-2nd & 3rd Floor slab completed.
- N21/F02-2nd & 3rd Floor slab completed.
- N22/F03-2nd Floor slab completed.
- N25/F06-1st Floor slab completed.
- N26/F07-1st Floor slab completed.



UPCOMING MILESTONES

- N23/F04-3rd Floor slab need to be complete
- N24/F05-3rd Floor slab need to be complete.
- N25/F06- 2nd & 3rd Floor slab need to be complete.
- N26/F07-3rd Floor slab need to be complete.

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
