

PROVIDENT **DEANSGATE**

Construction Updates

September 2026




Dear Esteemed Customer,

Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

*We are grateful for your kind cooperation.
Team Provident Deansgate*

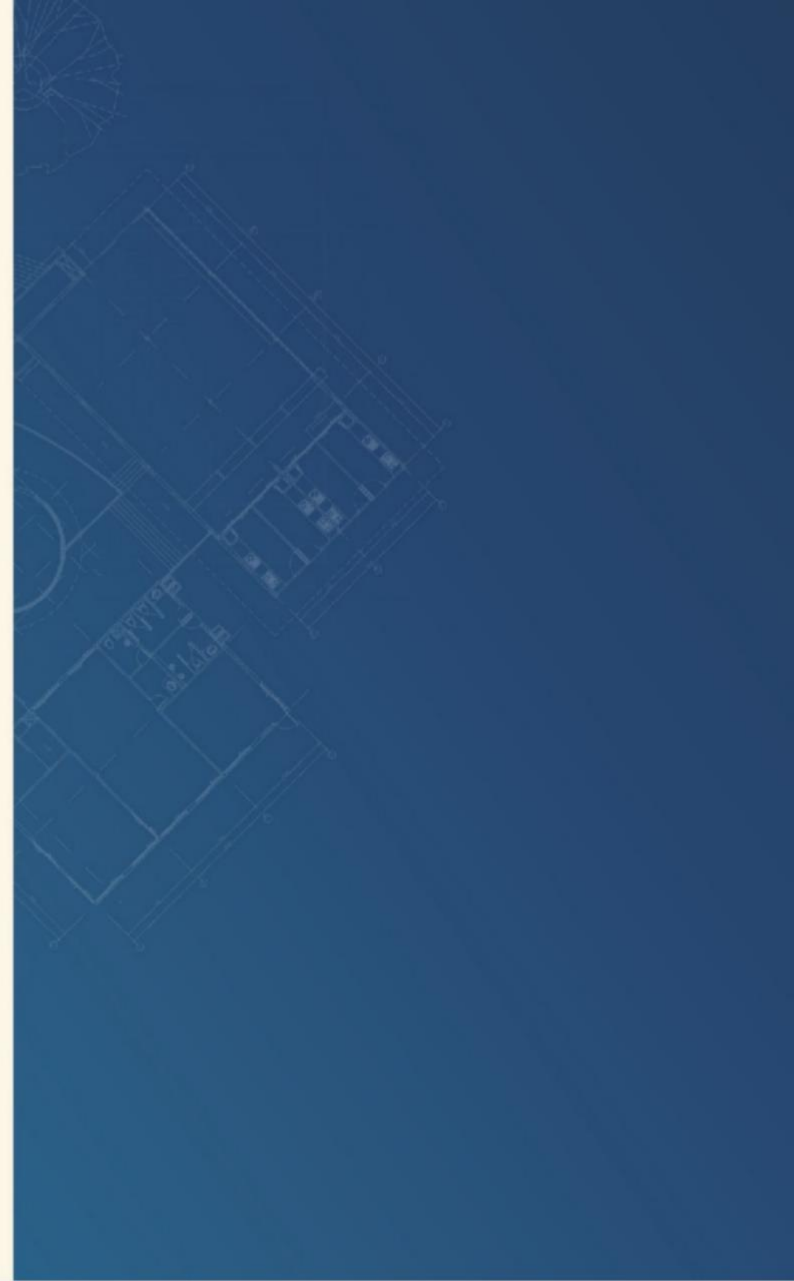



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER F (F14/S23 TO F08/S29)



Actual site photograph

PROGRESS TIMELINE



Aug'26



MILESTONES ACHIEVED

CLUSTER F STATUS

- S23-All work completed.
- S24-UPVC Window fixing completed & primer Work in progress.
- S25-Window fixing work need to start.
- S26- SF plastering & screed completed, Flooring work need to start. Backside External plastering work completed.
- S27-SF Internal plastering work completed & screed work need to start. GF putty work completed. Backside External plastering work & whitewash completed.
- S28-FF Plastering work completed & SF Electrical work in progress. Backside External plastering work & Whitewash work completed.
- S29-FF Plastering work completed & SF Electrical work completed . Plastering work need to start. Backside External plastering work& whitewash work completed.



UPCOMING MILESTONES

S29-Completion of Flooring need to be done.

CLUSTER H (H01/N27 TO H06/N32)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER H STATUS

- N27- SF block work in progress. GF & FF plastering work completed. Toilet plumbing work in progress.
- N28- SF block work in progress. GF & FF plastering work completed. Toilet plumbing work in progress.
- N29-TF Slab work completed. Construction of Block work completed. GF & FF plastering work completed. Toilet plumbing work in progress.
- N30-Construction of Block work completed. FF plastering work completed. Toilet plumbing work in progress.
- N31-Construction of Block work completed. FF plastering work completed. Toilet plumbing work in progress. GF & SF plastering work need to start.
- N32-Construction of Block work completed. FF plastering work completed. SF plastering work in progress. Toilet plumbing work in progress.



MILESTONES ACHIEVED

- N29/H3- 3rd Floor slab work completed.
- N29/H3- Construction of Block work completed.
- N30/H4- Construction of Block work completed.
- N31/H5- Construction of Block work completed.
- N32/H6- Construction of Block work completed.



UPCOMING MILESTONES

- N27/H1- Construction of Block work need o be complete.
- N28/H2- Construction of Block work need o be complete.

CLUSTER H (H12/S30 TO H07/S35)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER H STATUS

- S30-Construction of Block work completed. FF & GF plastering work completed. SF plastering work in progress.
- S31-Construction of Block work completed. FF & GF plastering work completed. SF plastering work need to start.
- S32-2nd floor Block work in progress. FF & GF plastering work completed.
- S33- SF block work need to start. FF Plastering work in progress. GF plastering work completed.
- S34- TF Slab completed. FF block work & plastering work completed.GF Block work completed & plastering work completed
- S35-TF Slab completed. FF block work in progress.. GF Block work completed & Plastering work in progress.



MILESTONES ACHIEVED

- S31/H11- Construction of wall completed.
- S34/H8-3rd Floor slab completed.
- S35/H7-3rd Floor slab completed.

UPCOMING MILESTONES

- S32/H10- Construction of wall to be complete
- S33/H19- Construction of wall to be complete

CLUSTER J (J17/N49 TO J20/N52)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER J STATUS

- N49- Construction of Block work completed. GF , FF & SF Plastering work completed. Backside External plastering work in progress.
- N50- Construction of Block work completed. GF , FF & SF Plastering work completed. backside External plastering work in progress.
- N51-Construction of Block work completed. GF,FF & SF plastering work completed. Backside external plastering work need to start.
- N52-Construction of Block work completed. GF,FF & SF plastering work completed. Backside External plastering need to start

 **MILESTONES
ACHIEVED**

 **UPCOMING
MILESTONES**

CLUSTER J (J10/N42 TO J13/N45)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER J STATUS

- N-42 –Plinth beam completed .Grade slab work completed.
- N43- Plinth beam completed .Grade slab completed.GF to FF Column completed.
- N-44 – Plinth beam completed & Grade slab work Completed. GF to FF Columns completed.
- N-45-1st & 2nd & 3rd Floor slab completed. GF&FF Block work completed. GF plastering work completed. FF plastering work need to start. SF block work need to start.



MILESTONES ACHIEVED



UPCOMING MILESTONES

CLUSTER J (J14/N46 TO J16/N48)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER J STATUS

- N-46 –GF & FF block work completed. GF plastering work completed. FF plastering work in progress. SF block work need to start.
- N-47 – GF & FF block work completed. GF plastering work completed. FF plastering work in progress. SF block work in progress.
- N-48-SF Block work in progress. FF plastering work in progress. GF plastering work completed.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N-48- Construction of Block work need to complete.
- N-47- Construction of Block work need to complete.

CLUSTER J (J01/N33 TO J05/N37)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER J STATUS

- N33-TF Slab completed.GF & FF Block work completed & GF plastering work completed. FF plastering work need to start.
- N34- TF Slab shuttering work in progress. GF & FF block work completed. GF plastering completed.
- N35- SF to TF Column work completed. TF slab work need to start. FF block work competed.GF plastering work completed.
- N36- SF Slab shuttering work need to start.GF Block work completed. GF Plastering work in progress.
- N37- FF to SF Columns completed. SF slab shuttering work need to start.GF Block work completed. GF plastering work need to start.



MILESTONES ACHIEVED

- N-33- TF Slab work completed.



UPCOMING MILESTONES

- N36/J4-2nd Floor slab to be complete.
- N37/J5-2nd Floor slab to be complete.
- N36/J4-3rd Floor slab to be complete.
- N37/J5-3rd Floor slab to be complete.
- N34/J2-3rd Floor slab to be complete.
- N35/J3-3rd Floor slab to be complete.

CLUSTER J (J06/N38 TO J09/N41)



Actual site photograph

CLUSTER J STATUS

- N38- SF Columns work completed. SF Slab work need to start.GF Block work completed.
- N39- SF Columns work completed. SF slab work need to start.GF Block work in progress.
- N40- Plinth beam completed. Grade slab work need to start.
- N41-Plinth beam completed. Grade slab work need to start.



MILESTONES ACHIEVED

- N40-Plinth beam completed.
- N41-Plinth beam completed.



UPCOMING MILESTONES

- N38- 2nd floor slab need to be Complete.
- N38- 3rd floor slab need to be Complete
- N39- 2nd floor slab need to be Complete
- N39- 3rd floor slab need to be Complete

PROGRESS TIMELINE



Aug'26

CLUSTER F (F1/N20 TO F7/N26)



Actual site photograph

PROGRESS TIMELINE



Aug'26

CLUSTER J STATUS

- N20- TF Slab completed.GF block work completed.GF plastering work in progress. FF block work in progress. SF Block work need to start.
- N21-TF Slab completed.GF block work completed.GF plastering work need to start. FF block work in progress.
- N22- TF Slab completed GF block work completed. GF plastering work need to start. FF block work in progress.
- N23-2nd & 3rd Floor slab completed.GF block work completed. FF block work need to start.
- N24- 2nd & 3rd Floor slab completed.GF block work completed. FF block work need to start.
- N25- 2nd Floor slab completed. 3rd slab work in progress.GF block work need to start.
- N26- 2nd Floor slab completed. 3rd slab work in progress.GF Block work need to start.



MILESTONES ACHIEVED

- N22/F03-3rd Floor slab completed.
- N23/F04-3rd Floor slab completed.
- N24/F05-3rd Floor slab completed.
- N25/F06-2nd Floor slab completed.
- N26/F07-2nd Floor slab completed.



UPCOMING MILESTONES

- N25/F06- 3rd Floor slab need to be complete.
- N26/F07-3rd Floor slab need to be complete.
- N20/F01-Construction of Block work need to be complete.

Site Office :**Provident Deansgate**

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited
No.8, Ulsoor Road, Bengaluru- 560 042
Tel: 080-44555544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
