

 **PROVIDENT
DEANSGATE**

Construction Updates

March 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Deansgate

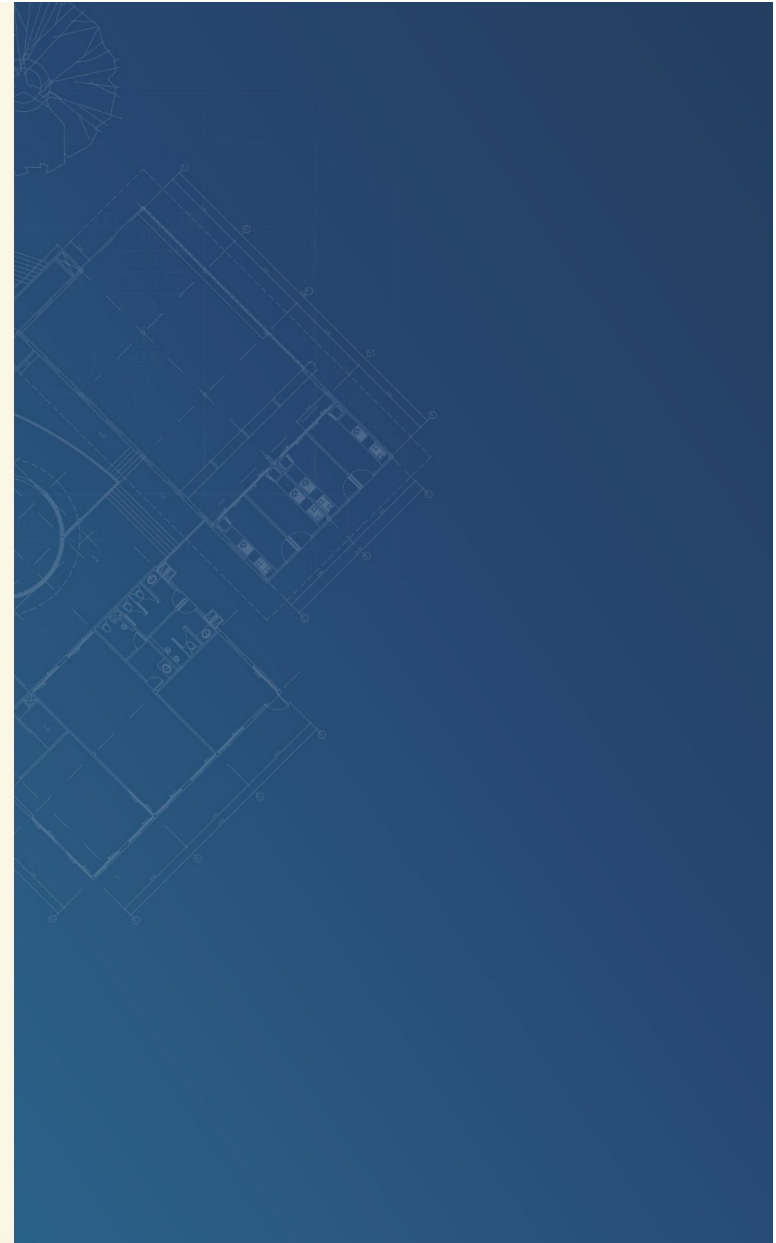



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER D (D1/N07)



Actual site photograph

CLUSTER D STATUS

- Handed over to Facility Team. Final Handing over completed.

 **MILESTONES ACHIEVED**

 **UPCOMING MILESTONES**

PROGRESS TIMELINE



March'26

CLUSTER D (D2/N06 to D4/N04)



Actual site photograph

PROGRESS TIMELINE



March'26

CLUSTER D STATUS

- N6 -Balcony & utility Flooring work completed. .GF ,FF, SF 1st Coat Internal putty work completed.
- N5 – Unit-2 Flooring completed & unit-3 SF Flooring work in progress. Internal putty work in progress
- N4 –Flooring work completed & Toilet flooring work in progress &External Cladding work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N4/D4 -Completion of Flooring to be completed.
- N5/D3 -Completion of Flooring to be completed.
- N6/D2 –Installation of External windows need to be complete.

CLUSTER D (D5/N03 TO D7/N01)



Actual site photograph

PROGRESS TIMELINE



March'26

CLUSTER D STATUS

- N1- FF & SF Flooring work completed. External cladding work in progress .Installation of External windows work in progress.
- N2- Flooring work completed, Installation of External windows work in progress
- N3-Flooring work completed, Installation of External windows work in progress



MILESTONES ACHIEVED

- N2/D6- Flooring work completed,
- N3/D5- Flooring work completed.



UPCOMING MILESTONES

- N1/D7-Floor tile to be completed & Installation of External windows need to be complete.
- N2/D6- Installation of External windows need to be complete.
- N3/D5-Installation of External windows need to be complete.

Cluster C (C1/N14 to C4/N11)



Actual site photograph

PROGRESS TIMELINE



March'26

Cluster C STATUS

- N11 –Putty work in progress & Installation of external windows completed.
- N12- Putty work in progress &Installation of external windows completed..
- N-13- Putty work in progress & Installation of external windows completed.
- N14- GF area Door fixed & SF Door work need to start. Putty work in progress .



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N13/C2- Installation of Door to be complete.
- N14/C1- Installation of Door to be complete.

Cluster C (C5/N10 to C7/N8)



Actual site photograph

Cluster C STATUS

- N8-External cladding work In progress & putty work in progress.
- N9 – Installation of external windows completed & putty work in progress
- N10- Installation of external windows completed & putty work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

PROGRESS TIMELINE



March'26

CLUSTER C (C8/S09 to C11/S12)



Actual site photograph

CLUSTER C STATUS

- S9 –Construction of Block work completed & FF plastering completed.
- S10- Construction of Block work completed & FF plastering need to be start.
- S11-FF Plastering completed. & SF Plastering need to be start
- S12-FF Plastering completed & SF Plastering need to be start.



MILESTONES ACHIEVED

- S9/C8-Construction of wall completed.
- S10/C9-Construction of wall completed.



UPCOMING MILESTONES

PROGRESS TIMELINE



March'26

CLUSTER C (C12/S13 to C14/S15)



Actual site photograph

CLUSTER C STATUS

- S13 - 2nd floor block work in progress.
- S14 - 2nd floor block work in progress.
- S15 - 2nd floor block work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- C12/S13 – Construction of wall to be complete.
- C13/S14 – Construction of wall to be complete.
- C14/S15 – Construction of wall to be complete.

PROGRESS TIMELINE



March'26

CLUSTER A (A12/S22 to A10/S20)



Actual site photograph

CLUSTER A STATUS

- S20-External plastering work completed & External Cladding work in progress.
- S21-Front side External plastering work completed & Backside external plastering work in progress. External Cladding work completed.
- S22-External plastering work completed & External Cladding work completed.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- S22/A12 –Floor tiling to be completed

PROGRESS TIMELINE



March'26

CLUSTER A (A06/S16 to A09/S19)



Actual site photograph

CLUSTER A STATUS

- S16- SF Electrical work in progress & FF internal plastering completed & FF Screed completed.
- S17 - SF Electrical work in progress. FF internal plaster work need to be start.
- S18 - SF Electrical work in progress. FF internal plaster work in progress
- S19 – External plastering work in progress & FF internal plaster work completed.



MILESTONES ACHIEVED



UPCOMING MILESTONES

PROGRESS TIMELINE



March'26

CLUSTER A (A01/N19 to A05/N15)



Actual site photograph

PROGRESS TIMELINE



March'26

CLUSTER A STATUS

- N15- Construction of block work completed and FF Internal plastering completed.
- N16- Construction of block work completed and FF Internal plastering completed.
- N17- Construction of block work completed & FF internal plastering completed . External plastering work in progress.
- N18- External plastering completed .
- N19-External plastering completed & SF Internal plastering need to be complete.



MILESTONES ACHIEVED

- A03/N17- Construction of wall completed.
- A04/N16- Construction of wall completed.
- A05/N15- Construction of wall completed.



UPCOMING MILESTONES

CLUSTER D (D15/S08 to D12/S05)



Actual site photograph

CLUSTER D STATUS

- S5-SF Internal plastering work in progress & FF Screed completed.
- S6-SF Internal plastering work in progress & FF Screed completed.
- S7-External plastering Work in progress.
- S8- External plastering Work need to be start.



MILESTONES ACHIEVED



UPCOMING MILESTONES

PROGRESS TIMELINE



March'26

CLUSTER D (D11/S04 to D08/S01)



Actual site photograph

CLUSTER D STATUS

- S1-FF Tile flooring completed & GF Flooring work in progress. Internal plastering completed
- S2-FF Tile flooring & Internal plastering completed , GF Flooring need to start.
- S3- FF Screed completed & FF Tile flooring need to start..
- S4- internal plastering completed.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- S01/D8 -Floor tiling to be completed .
- S02/D9 -Floor tiling to be completed

PROGRESS TIMELINE



March'26

CLUSTER B (B02/E07 to B04/E05)



Actual site photograph

CLUSTER B STATUS

- E7-External cladding work in progress.
- E6-External cladding work in progress.
- E5-External cladding work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- B02/E07 –Completion of Flooring need to be done.

PROGRESS TIMELINE



March'26

CLUSTER B (B05/E04 to B08/E01)



Actual site photograph

PROGRESS TIMELINE



March'26

CLUSTER B STATUS

- E1- Construction of block work completed. External plastering completed . External cladding & FF Internal plastering work in progress
- E2-Construction of block work completed. External plastering completed. External cladding & FF Internal plastering work in progress
- E3- External plastering completed & External cladding work in progress.
- E4- External plastering completed & External cladding work in progress



MILESTONES ACHIEVED

- B08/E01- Construction of wall completed
- B07/E02- Construction of wall completed
- B06/E03- Construction of wall completed
- B05/E04- Construction of wall completed



UPCOMING MILESTONES

CLUSTER B (W1/B1)



Actual site photograph

PROGRESS TIMELINE



March'26

CLUSTER B STATUS

- W1- FF Block work completed & SF block work in progress.



MILESTONES ACHIEVED



UPCOMING MILESTONES

- B01/W01 –Construction of wall need to be completed.

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-4455544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/041123/006373
