

# **PROVIDENT DEANSGATE**

## **Construction Updates**

December 2025



*Dear Esteemed Customer,*


*Greetings from Provident*

*It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.*

*We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.*

*We are grateful for your kind cooperation.*

*Team Provident Deansgate*







# Provident Deansgate

IVC Road, Bengaluru



## Construction Updates

Overall view



# CLUSTER F (F14/S23 TO F08/S29)



## CLUSTER STATUS

- S23-Skirting Work in progress
- S24-External wall cladding work in progress & toilet waterproofing in progress.
- S25-SF Block work in progress.
- S26-SF Block work in progress.
- S27-3<sup>rd</sup> Floor slab work completed. FF block work in progress.
- S28-3<sup>rd</sup> Floor slab work in progress.
- S29-3<sup>rd</sup> Floor slab work in progress. GF block work in progress



## MILESTONES ACHIEVED

- S26/F11 Construction of Wall Completed.
- S27/F10 3<sup>rd</sup> Floor slab work Completed..
- S28/F9 2<sup>nd</sup> Floor slab work Completed.
- S29/F8 2<sup>nd</sup> Floor slab work Completed.

## PROGRESS TIMELINE



Nov 25

Dec 25



## UPCOMING MILESTONES

- S23/F14 Completion of Flooring, Windows & Doors to be complete.
- S24/F13 Completion of Flooring, Windows & Doors to be complete.
- S25/F12 Construction of Wall to be Complete
- S26/F11 Construction of Wall to be Complete.
- S27/F10 Construction of Wall to be Complete.
- S28/F9 3<sup>rd</sup> Floor slab work to be Complete.
- S29/F8 3<sup>rd</sup> Floor slab work to be Complete

# CLUSTER H (H01/N27 TO H06/N32)



## CLUSTER STATUS

- N27-1<sup>st</sup> Floor slab work in progress
- N28-1<sup>st</sup> floor slab work in progress
- N29-1<sup>st</sup> floor slab work in progress
- N30-1<sup>st</sup> floor slab work in progress
- N31-1<sup>st</sup> floor slab work in progress
- N32-2<sup>nd</sup> floor column work in progress



## MILESTONES ACHIEVED

- N32/H6- 1<sup>st</sup> Floor slab work Completed



## UPCOMING MILESTONES

- N29/H3- 1<sup>st</sup> Floor slab work to be Complete
- N30/H4- 1<sup>st</sup> Floor slab work to be Complete
- N31/H5- 1<sup>st</sup> Floor slab work to be Complete
- N32/H6- 2<sup>nd</sup> Floor slab work to be Complete

## PROGRESS TIMELINE



Nov 25

Dec 25



# CLUSTER H (H12/S30 TO H07/S35)



## CLUSTER STATUS

- S30- 1<sup>st</sup> Floor slab work in progress
- S31- 1<sup>st</sup> Floor slab work in progress
- S32-1<sup>st</sup> Floor column completed & slab work in progress
- S33-Plinth beam work in progress
- S34-Plinth beam work in progress
- S35-Plinth Beam work in progress



## MILESTONES ACHIEVED

- S32/H10-Plinth Beam work Completed



## UPCOMING MILESTONES

- S30/H12-1<sup>st</sup> Floor slab work to be Complete
- S31/H11-1<sup>st</sup> Floor slab work to be Complete
- S32/H10-1<sup>st</sup> Floor slab work to be Complete
- S33/H9-Plinth beam work to be complete& 1<sup>st</sup> Floor slab work to be Complete
- S34/H8-Plinth beam work to be complete
- S35/H7-Plinth beam work to be complete


## PROGRESS TIMELINE



Nov 25

Dec 25

# CLUSTER J (J1/N33 TO J4/N36)

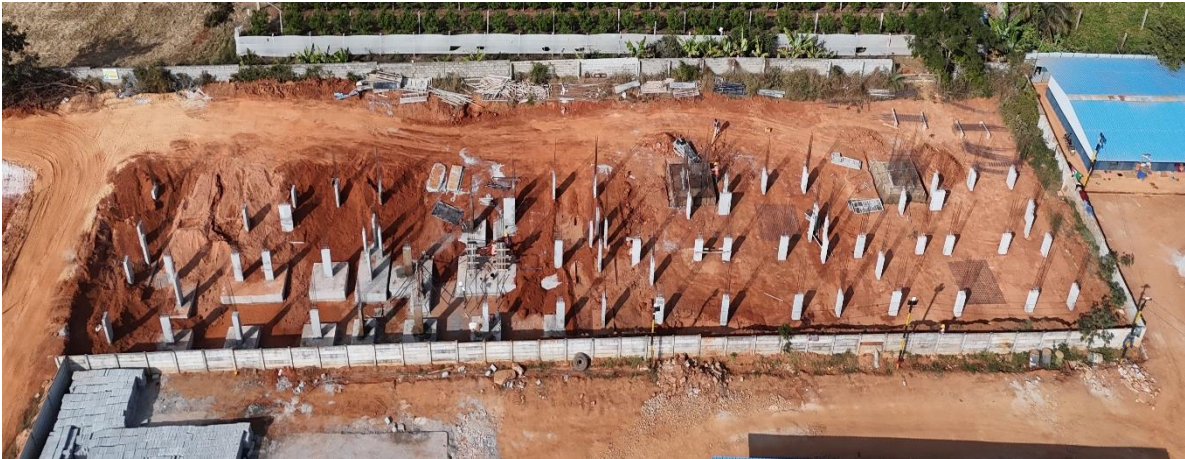

## PROGRESS TIMELINE



Nov 25



Dec 25

Actual site photograph

## CLUSTER STATUS

- N33- Backfilling work in progress
- N34- Backfilling work in progress
- N35- Backfilling work in progress
- N36- Backfilling work in progress



## MILESTONES ACHIEVED

- N34/J2-Excavation work completed
- N35/J3-Excavation work completed
- N36/J4-Excavation work completed



## UPCOMING MILESTONES

- N33/J1-Plinth beam work to be complete
- N34/J2-Plinth beam work to be complete
- N35/J3-Plinth beam work to be complete
- N36/J4-Plinth beam work to be complete



# CLUSTER J (J5/N37 TO J11/N43)



## CLUSTER STATUS

- N-37 Excavation completed & Footing work in progress
- N-38 Excavation completed & Footing work in progress
- N-39 Excavation work completed
- N-40-Excavation work completed
- N-41 Excavation work completed
- N-42 Excavation work completed
- N-43 Excavation work completed & Footing work in progress



## MILESTONES ACHIEVED

- N37/J5-Excavation work completed
- N38/J6-Excavation work completed
- N39/J7-Excavation work completed



## UPCOMING MILESTONES

- N37/J5-Plinth beam work to be complete
- N38/J6-Plinth beam work to be complete

## PROGRESS TIMELINE



●  
Nov 25

●  
Dec 25



# CLUSTER J (J12/N44 TO J20/N52)



## CLUSTER STATUS

- N44- Footing work Completed
- N45- Footing work Completed
- N46- Footing work Completed
- N47- Footing work Completed
- N48- Footing work in progress
- N49- Backfilling work in progress.
- N50- Backfilling completed , plinth beam in progress.
- N51- Plinth beam work completed.
- N52- Footing work in progress.



## MILESTONES ACHIEVED

- N51/J19-Plinth beam work completed
- N52/J20-Excavation work completed



## UPCOMING MILESTONES

- N48/J16-Plinth beam work to be complete
- N49/J17-Plinth beam work to be complete
- N50/J18-Plinth beam work to be complete

## PROGRESS TIMELINE



Nov 25

Dec 25

# Contact Us



## Site Office :

### Provident Deansgate

Uganawadi circle, Devanahalli Taluk,  
Bengaluru - 562110.

## Regional Office :

Provident Housing Limited  
No.8, Ulsoor Road, Bengaluru- 560 042  
Tel: 080-44555544

**Email :** [crm@providenthousing.com](mailto:crm@providenthousing.com) (Subject line - Project name/ unit number)

**Call Us :** +91 - 80-67724001 / 1 860 208 0000

**Web :** [www.providenthousing.com](http://www.providenthousing.com)

## RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
