

 PROVIDENT
DEANSGATE

Construction Updates

October 2025



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Deansgate





Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER F (F14/S23 TO F08/S29)



CLUSTER STATUS

- S23-Plastering Work in progress
- S24-Block work in progress
- S25-3rd floor slab work in progress
- S26-3rd floor slab work in progress
- S27-2nd Floor slab work in progress
- S28-2nd Floor slab work in progress
- S29-1st Floor slab work in progress



MILESTONES ACHIEVED

- S23/F14 construction of walls Completed
- S24/F13 3rd Floor slab work Completed
- S25/F12 2nd Floor slab work Completed
- S26/F11 2nd Floor slab work Completed.
- S27/F10 1st Floor slab work Completed.
- S28/F9 1st Floor slab work Completed.
- S29/F8 Plinth Beam work Completed.

PROGRESS TIMELINE



Sep 25



Oct 25



UPCOMING MILESTONES

- S23/F14 Completion of Flooring to be complete
- S24/F13 Construction of Wall to be complete . .
- S25/F12 3rd Floor slab work to be Complete
- S26/F11 3rd Floor slab work to be Complete.
- S27/F10 2nd Floor slab work to be Complete
- S28/F9 2nd Floor slab work to be Complete.
- N29/F8 1st Floor slab work to be Complete.

CLUSTER H (H01/N27 TO H06/N32)



CLUSTER STATUS

- N27-Plinth beam work in progress
- N28-1st floor slab work in progress
- N29-1st floor slab work in progress
- N30-1st floor slab work in progress
- N31-1st floor slab work in progress
- N32-1st floor slab work in progress



MILESTONES ACHIEVED

- N28/H2-Plinth beam Completed
- N29/H3-Plinth beam Completed



UPCOMING MILESTONES

- N27/H1-Plinth beam to be complete.


PROGRESS TIMELINE



Sep 25

Oct 25

CLUSTER H (H12/S30 TO H07/S35)

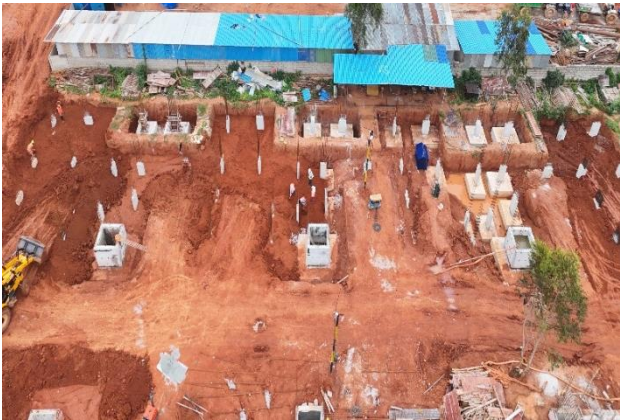

CLUSTER STATUS

- S30- Back filling work in progress
- S31- Backfilling work in progress
- S32-Backfilling work in progress
- S33-Backfilling work in progress
- S34-Backfilling work in progress
- S35-Plinth Beam work in progress



MILESTONES ACHIEVED



UPCOMING MILESTONES

- S30/H12-Plinth beam work to be complete
- S31/H11-Plinth beam work to be complete
- S32/H10-Plinth beam work to be complete

PROGRESS TIMELINE



Sep 25

Oct 25

CLUSTER J (J1/N33 TO J4/N36)



CLUSTER STATUS

- N50- Footing work in progress
- N51- Footing work in progress
- N47- Excavation work in progress
- N48- Excavation work in progress
- N49- Excavation work in progress



MILESTONES ACHIEVED

- N33/J1-Excavation work completed



UPCOMING MILESTONES

- N34/J2-Excavation work to be complete
- N35/J3-Excavation work to be complete
- N36/J4-Excavation work to be complete

PROGRESS TIMELINE



Actual site photograph

CLUSTER J (J5/N37 TO J11/N43)



CLUSTER STATUS

- N-37 Excavation to be start



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N37/J5-Excavation work to be complete

PROGRESS TIMELINE



Oct 25

Actual site photograph

CLUSTER J (J12/N44 TO J20/N52)



CLUSTER STATUS

- N44- Excavation work in progress
- N545- Excavation work in progress
- N46- Footing work in progress
- N47- Footing work in progress
- N48- Footing work in progress
- N49- Footing work in progress
- N50- Footing work in progress
- N51- Plinth beam work in progress
- N52- Excavation work in progress



MILESTONES ACHIEVED

- N46/J14-Excavation work completed
- N47/J15-Excavation work completed
- N48/J16-Excavation work completed



UPCOMING MILESTONES

- N44/J12-Excavation work to be complete
- N45/J13-Excavation work to be complete
- N51/J19-Plinth beam work to be complete
- N52/J20-Excavation work to be complete

PROGRESS TIMELINE



Sep 25

Oct 25

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru - 562110.

Regional Office :

Provident Housing Limited
No.8, Ulsoor Road, Bengaluru- 560 042
Tel: 080-44555544

Email : crm@providenthousing.com (Subject line - Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
