

 **PROVIDENT  
DEANSGATE**

**Construction Updates**

April 2026



*Dear Esteemed Customer,*


*Greetings from Provident*

*It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.*

*We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.*

*We are grateful for your kind cooperation.*

*Team Provident Deansgate*

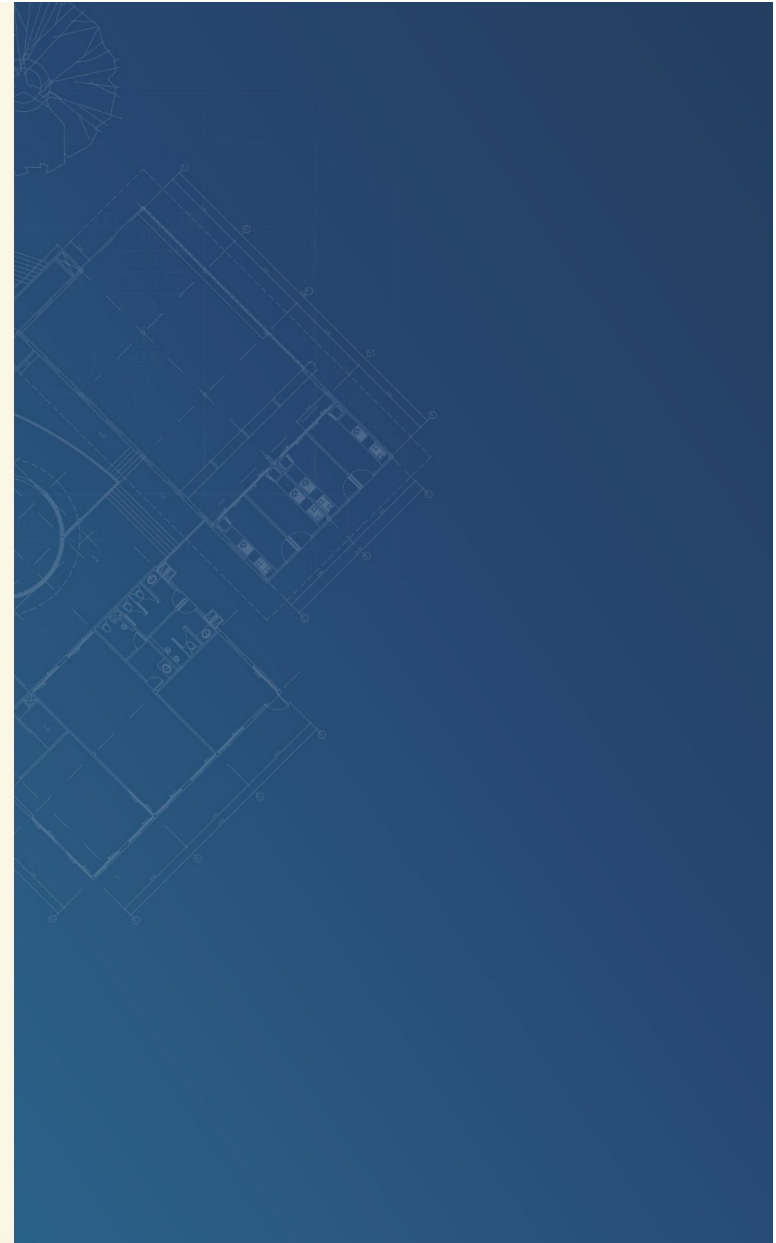



# Provident Deansgate

IVC Road, Bengaluru



## Construction Updates

Overall view

## CLUSTER F (F14/S23 TO F08/S29)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER F STATUS

- S23-All work completed.
- S24-UPVC Window fixing completed & primer Work in progress.
- S25-External cladding completed & window fixing need to start.
- S26- FF putty work completed & SF Flooring need to start.
- S27-SF Internal plastering work in progress .GF putty work in progress.
- S28-FF electrical work Completed & FF Plastering need to start. SF Electrical work in progress.
- S29-FF electrical work Completed & FF Plastering need to start. SF Electrical work in progress.



### MILESTONES ACHIEVED

- S24/F13 Installation of External Windows completed .



### UPCOMING MILESTONES

## CLUSTER H (H01/N27 TO H06/N32)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER H STATUS

- N27- FF Block work completed & SF to TF Columns completed & TF Slab shuttering need to start.
- N28- FF Block work completed & SF to TF Columns completed .
- N29-SF to TF Columns work completed & FF Block work need to start.
- N30-2<sup>nd</sup> floor Slab Work in progress.
- N31-FF to SF Columns work completed . SF Slab work need to start.
- N32-FF to SF Columns work completed . SF Slab work need to start.



### MILESTONES ACHIEVED



### UPCOMING MILESTONES

- N30/H4- 2<sup>nd</sup> Floor slab work to be Complete
- N31/H5- 2<sup>nd</sup> Floor slab work to be Complete

## CLUSTER H (H12/S30 TO H07/S35)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER H STATUS

- S30- FF block work completed & GF Electrical work in progress
- S31-FF block work completed & GF Electrical work in progress
- S32-3<sup>rd</sup> Floor slab work in progress & GF Block work completed.
- S33- 2<sup>nd</sup> Floor slab work completed & FF Columns work in progress & GF Block work completed.
- S34-FF to SF Columns completed & GF Block work need to start.
- S35-FF to SF Columns work completed .



### MILESTONES ACHIEVED

S33/H9- 2<sup>nd</sup> Floor slab Completed.

### UPCOMING MILESTONES

- S34/H8-2<sup>nd</sup> Floor slab work to be Complete.
- S35/H7-2<sup>nd</sup> Floor slab work to be Complete.
- S33/H9-2<sup>nd</sup> Floor slab work to be Complete.
- S32/H10-3<sup>rd</sup> Floor slab work to be Complete.
- S33/H9-3<sup>rd</sup> Floor slab work to be Complete
- S30/H12- Construction of wall to be complete

## CLUSTER J (J17/N49 TO J20/N52)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER J STATUS

- N49- FF Slab completed & SF Slab shuttering & Reinforcement work in progress.
- N50- FF Slab completed & SF Slab shuttering & Reinforcement work in progress.
- N51- FF Slab completed & FF to SF Columns work completed .
- N52-FF Slab completed & FF to SF Columns work in progress.

### MILESTONES ACHIEVED

- N49/J17-1<sup>st</sup> Floor slab complete.
- N50/J18-1<sup>st</sup> Floor slab complete.
- N51/J19-1<sup>st</sup> Floor slab complete.
- N52/J20-1<sup>st</sup> Floor slab complete.

### UPCOMING MILESTONES

- N49/J17-2<sup>nd</sup> Floor slab to be complete.
- N50/J18-2<sup>nd</sup> Floor slab to be complete.
- N51/J19-2<sup>nd</sup> Floor slab to be complete.
- N52/J20-2<sup>nd</sup> Floor slab to be complete.

## CLUSTER J (J16/N48 TO J10/N42)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER J STATUS

- N-48- Plinth beam Work & Grade slab completed. FF Columns work in progress.
- N-47 – Plinth beam Work completed & Grade slab work in progress.
- N-46 –Plinth beam completed & curing work in progress.
- N-45-Plinth beam PCC Work in progress.
- N-44 –Backfilling work completed & Plinth beam PCC need to start.
- N-43 -Back filling work in progress
- N-42 - Back filling work in progress



### MILESTONES ACHIEVED

- N48/J16-Plinth beam completed.
- N47/J15-Plinth beam completed.



### UPCOMING MILESTONES

- N48/J16-1<sup>st</sup> Floor slab to be complete
- N47/J15-1<sup>st</sup> Floor slab to be complete
- N46/J14- Plinth beam need to complete.

## CLUSTER J (J09/N41 TO J01/N33)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER J STATUS

- N41- Footing work completed & Back filling work in progress
- N40- Footing work completed & Back filling work in progress
- N39- Plinth beam completed & Grade slab work in progress.
- N38- Grade slab Completed & Columns work in progress.
- N37-FF Slab shuttering and reinforcement work in progress.
- N36- 1<sup>st</sup> floor slab work in progress.
- N35-FF to SF Columns completed.
- N34-FF to SF Columns Completed.
- N33- GF to FF Columns work in progress.



### MILESTONES ACHIEVED

- N39/J07- Plinth beam completed.



### UPCOMING MILESTONES

- N33/J1-1<sup>st</sup> Floor slab to be complete.
- N40/J8- Plinth beam need to be Complete.
- N36/J4-1<sup>st</sup> Floor slab to be complete.
- N37/J5-1<sup>st</sup> Floor slab to be complete.
- N38/J6-1<sup>st</sup> Floor slab to be complete.

## CLUSTER F (F1/N20 TO F7/N26)



Actual site photograph

### PROGRESS TIMELINE



April'26

### CLUSTER J STATUS

- N20- Back filling Completed & Plinth beam PCC Work need to start.
- N21- Footing work completed & Backfilling work in progress.
- N22- Footing work completed & Backfilling work in progress .
- N23-Footing work completed & Backfilling work in progress .
- N24- Footing work completed & Backfilling work in progress .
- N25- Footing work completed & Backfilling work in progress .
- N25- Footing work completed & Backfilling work in progress .



### MILESTONES ACHIEVED



### UPCOMING MILESTONES

- N20/F01-Plinth beam work to be completed.

## Contact Us



### **Site Office :**

#### **Provident Deansgate**

Uganawadi circle, Devanahalli Taluk,  
Bengaluru – 562110.

### **Regional Office :**

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-4455544

**Email :** [crm@providenthousing.com](mailto:crm@providenthousing.com) (Subject line – Project name/ unit number)

**Call Us :** +91 - 80-67724001 / 1 860 208 0000

**Web :** [www.providenthousing.com](http://www.providenthousing.com)

### **RERA Registration Number :**

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
