

 **PROVIDENT
DEANSGATE**

Construction Updates

May 2026




Dear Esteemed Customer,

Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

*We are grateful for your kind cooperation.
Team Provident Deansgate*

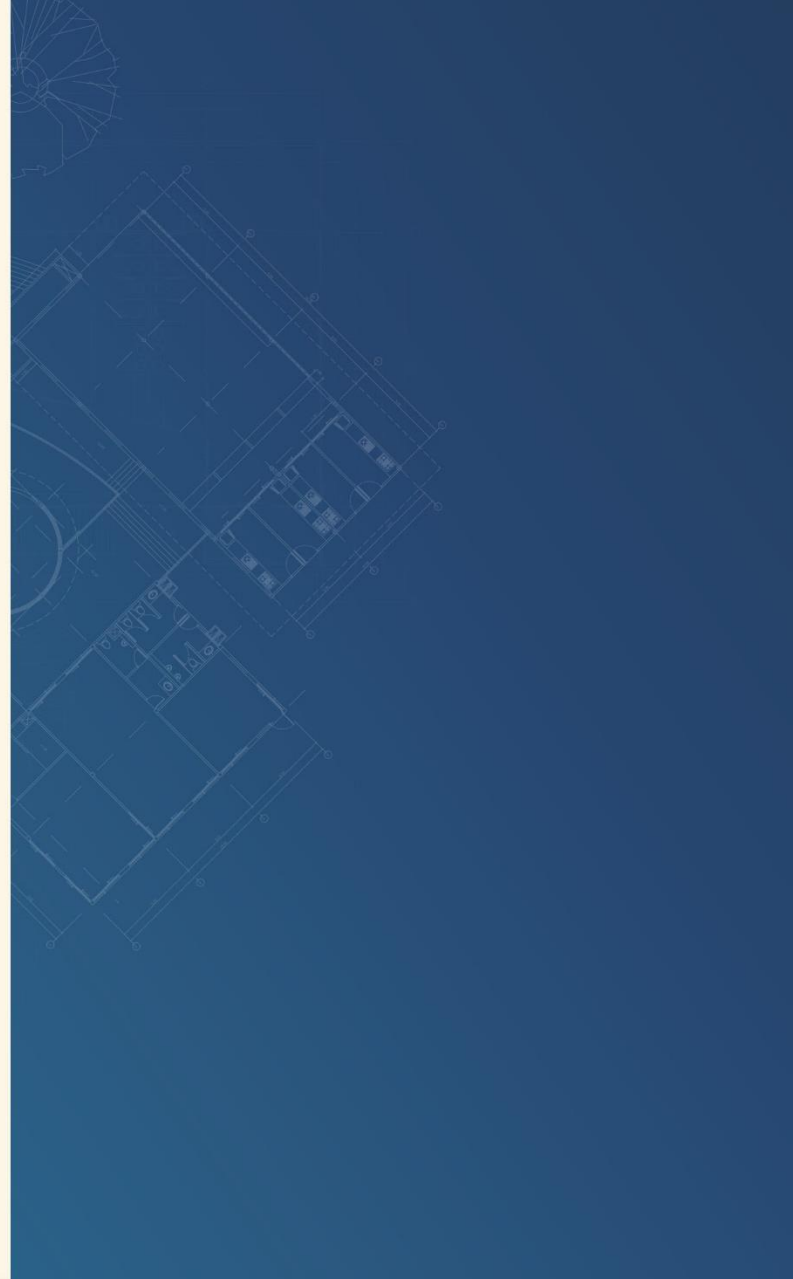



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER F (F14/S23 TO F08/S29)



Actual site photograph

PROGRESS TIMELINE



May'26



MILESTONES ACHIEVED

CLUSTER F STATUS

- S23-All work completed.
- S24-UPVC Window fixing completed & primer Work in progress.
- S25-Window fixing work need to start.
- S26- SF plastering & screed completed, Flooring need to start.
- S27-SF Internal plastering work completed & screed work need to start. GF putty work in progress.
- S28-FF electrical work Completed & FF Plastering work in progress, SF Electrical work in progress.
- S29-FF Plastering completed. SF Electrical work in progress.



UPCOMING MILESTONES

CLUSTER H (H01/N27 TO H06/N32)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER H STATUS

- N27- FF Block work completed .TF Slab shuttering need to start.
- N28- FF Block work completed & SF to TF Columns completed .
- N29-2nd floor Slab completed & TF Columns work in progress & FF Block work need to start.
- N30-2nd floor Slab completed.
- N31-2nd floor Slab completed.
- N32-SF Slab work in progress.



MILESTONES ACHIEVED

- N29/H3- 2nd Floor slab Completed.
- N30/H4- 2nd Floor slab Completed.
- N31/H5- 2nd Floor slab Completed.



UPCOMING MILESTONES

- N32/H6- 2nd Floor slab work to be Complete.
- N27/H1- 3rd Floor slab work to be complete.
- N28/H2- 3rd Floor slab work to be complete.

CLUSTER H (H12/S30 TO H07/S35)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER H STATUS

- S30- FF block work completed & GF Electrical work in progress
- S31-FF block work completed & GF Electrical work in progress
- S32-3rd Floor slab work in progress & GF Block work completed.
- S33- 2nd floor slab completed. & TF Columns work in progress..
- S34- 2nd floor slab work in progress. GF Block work need to start.
- S35-FF to SF Columns work completed & SF Slab work need to start, GF Block work need to start.



MILESTONES ACHIEVED

UPCOMING MILESTONES

- S34/H8-2nd Floor slab work to be Complete.
- S35/H7-2nd Floor slab work to be Complete..
- S32/H10-3rd Floor slab work to be Complete.
- S33/H9-3rd Floor slab work to be Complete
- S30/H12- Construction of wall to be complete

CLUSTER J (J17/N49 TO J20/N52)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER J STATUS

- N49- FF, SF, & TF Slab completed . TF Slab curing in progress.GF Block work need to start.
- N50- SF Slab completed & TF Columns reinforcement work in progress.
- N51- SF Slab completed & slab curing work in progress.
- N52-FF to SF Columns completed & SF Slab work in progress.



MILESTONES ACHIEVED

- N49/J17-2nd & 3rd Floor slab completed.
- N50/J18-2nd Floor slab completed.
- N51/J19-2nd Floor slab completed.



UPCOMING MILESTONES

- N50/J18-3rd Floor slab to be complete.
- N51/J19-3rd Floor slab to be complete.
- N52/J20-2nd & 3rd Floor slab to be complete.

CLUSTER J (J16/N48 TO J10/N42)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER J STATUS

- N-48- 1st Floor slab complete & SF Columns work in progress.
- N-47 –1st Floor slab work in progress.
- N-46 –FF Columns completed & FF Slab work need to start.
- N-45-Plinth beam completed & Grade slab completed. FF Columns work in progress.
- N-44 – Plinth beam reinforcement completed & shuttering work in progress.
- N-43 -Plinth beam reinforcement completed & shuttering work in progress.
- N-42 –Plinth beam reinforcement work in progress.



MILESTONES ACHIEVED

- N48/J16- 1st Floor slab completed.
- N45/J13- Plinth beam completed.
- N46/J14- Plinth beam completed.



UPCOMING MILESTONES

- N48/J16-2nd Floor slab to be complete
- N47/J15-1st Floor slab to be complete
- N46/J14- 1st Floor slab to be complete
- N45/J13-1st Floor slab to be complete
- N44/J12 – Plinth beam to be complete.
- N43/J11 – Plinth beam to be complete.
- N42/J10 – Plinth beam to be complete.

CLUSTER J (J09/N41 TO J01/N33)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER J STATUS

- N41-Plinth beam reinforcement completed & shuttering work in progress.
- N40- Plinth beam reinforcement completed & shuttering work in progress.
- N39- 1st Floor slab work in progress.
- N38- 1st Floor slab completed & SF Columns work in progress.
- N37- 1st Floor slab completed & SF Columns work in progress .
- N36- 1st Floor slab completed & SF Columns work completed & SF Slab work need to start.
- N35-SF Columns work completed & SF Slab work need to start.
- N34-FF to SF Columns Completed & SF Slab work need to start.
- N33-1st Slab work in progress.



MILESTONES ACHIEVED

- N36/J4-1st Floor slab completed.
- N37/J5-1st Floor slab completed.
- N38/J6-1st Floor slab completed.



UPCOMING MILESTONES

- N33/J1-1st Floor slab to be complete.
- N40/J8- Plinth beam need to be Complete.
- N41/J9- Plinth beam need to be Complete.
- N39/J7-1st Floor slab to be complete.
- N40/J8-1st Floor slab to be complete.
- N41/J9-1st Floor slab to be complete.

CLUSTER F (F1/N20 TO F7/N26)



Actual site photograph

PROGRESS TIMELINE



May'26

CLUSTER F STATUS

- N20- Plinth beam Completed
- N21-Plinth beam reinforcement work completed & shuttering work need to start.
- N22- Plinth beam reinforcement work completed & shuttering work need to start.
- N23-Plinth beam PCC work in progress.
- N24- Footing work completed & Backfilling work in progress .
- N25- Footing work completed & Backfilling work in progress .
- N26- Footing work completed & Backfilling work in progress .



MILESTONES ACHIEVED

- N20/F01-Plinth beam completed.



UPCOMING MILESTONES

- N21/F02-Plinth beam work to be complete.

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-4455544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
