

 **PROVIDENT
DEANSGATE**

Construction Updates

February 2026



Dear Esteemed Customer,


Greetings from Provident

It gives us immense pleasure to update you through this edition of Provident Newsletter and provide you with the latest information about your home in Provident Deansgate. As we move ahead, we at Provident sincerely thank you for your continual faith and trust reposed in the brand.

We are happy to inform you that the construction and infrastructure works at the site is progressing well. We thank you for your understanding that is a construction site with extensive debris, heavy vehicular movement, uneven surfaces and hence keeping in mind your safety, visits to this site is restricted. You may seek prior approval and we can accommodate the scheduled visit from your respective banker.

We are grateful for your kind cooperation.

Team Provident Deansgate

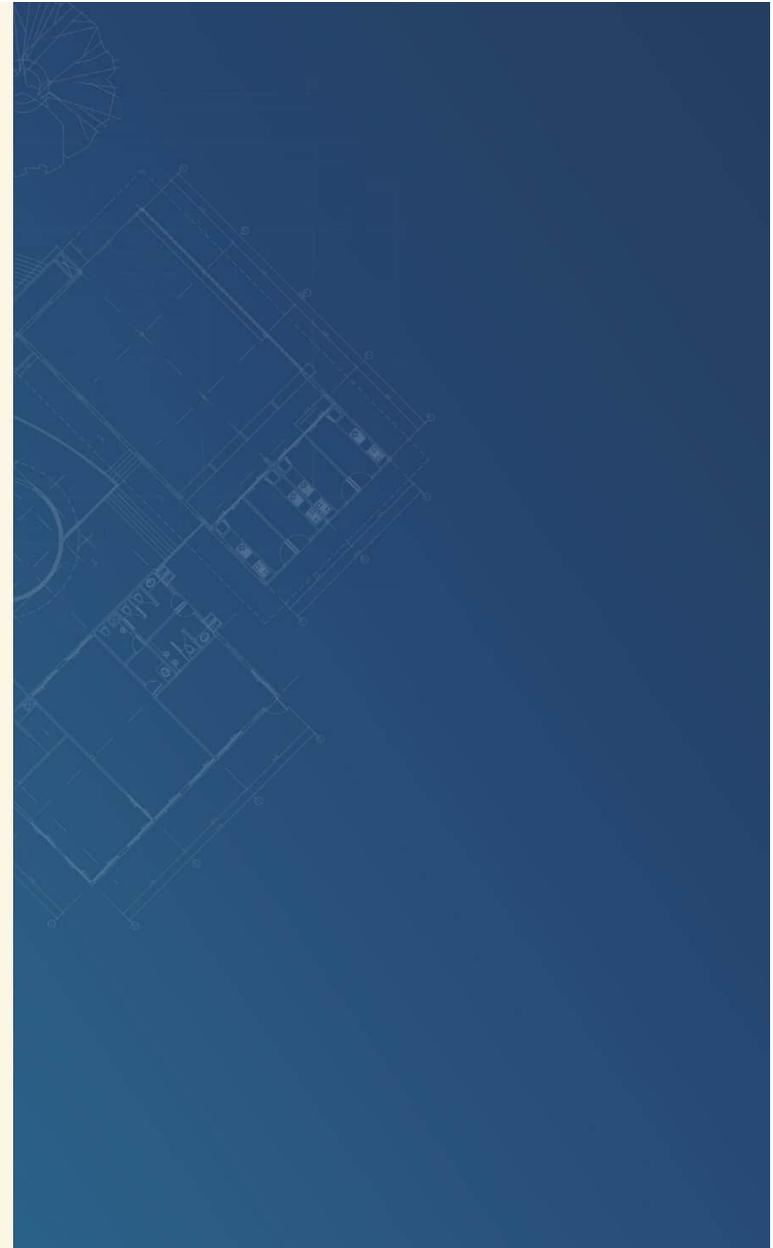



Provident Deansgate

IVC Road, Bengaluru



Construction Updates

Overall view

CLUSTER F (F14/S23 TO F08/S29)



Actual site photograph

PROGRESS TIMELINE



February'26

CLUSTER F STATUS

- S23-Internal ceiling & interior Work in progress
- S24-Internal tile flooring completed & primer Work in progress.
- S25-Internal & External plastering work completed & GF flooring completed & FF Flooring work in progress.
- S26-Construction of Block work completed & GF & FF Internal plastering completed & SF internal plastering work in progress.
- S27-Construction of Block work completed .
- S28-FF Block work Completed & plastering work in progress & SF Block work WIP..
- S29-FF Block work Completed & plastering work in progress.



MILESTONES ACHIEVED

- S24/F13 flooring work Completed.
- S26/F11 Construction of Wall Completed.
- S27/F10 Construction of Wall Completed



UPCOMING MILESTONES

- S24/F13 Installation of, Windows & Doors to be complete.
- S25/F12 flooring work to be complete.
- S28/F9 Construction of Wall to be Complete.
- S29/F8 Construction of Wall to be Complete

CLUSTER H (H01/N27 TO H06/N32)



Actual site photograph

PROGRESS TIMELINE



February'26

CLUSTER H STATUS

- N27-1st Floor slab completed. & SF Slab work in progress .
- N28-1st floor slab completed & GF block work completed.
- N29-2nd floor column completed & GF block work completed.
- N30-2nd floor column completed & GF block work completed..
- N31-2nd floor slab work in progress.
- N32-2nd floor slab work in progress.



MILESTONES ACHIEVED

- N27/H1- 1st Floor slab work Completed
- N28/H2- 1st Floor slab work Completed



UPCOMING MILESTONES

- N27/H1- 2nd Floor slab work to be Complete
- N28/H2- 2nd Floor slab work to be Complete
- N27/H1- 3rd Floor slab work to be Complete

CLUSTER H (H12/S30 TO H07/S35)



Actual site photograph

PROGRESS TIMELINE



February'26

CLUSTER H STATUS

- S30- GF block work completed.
- S31- GF block work in progress.
- S32-3rd Floor slab work in progress.
- S33- 1st Floor slab completed.
- S34-1st Floor slab work in progress
- S35-1st Floor slab work in progress.



MILESTONES ACHIEVED

- S30/H12-3rd Floor slab work Completed
- S31/H11-2nd Floor slab work Completed
- S32/H10-2nd Floor slab work Completed.
- S33/H9- 1st Floor slab completed



UPCOMING MILESTONES

- S31/H11-3rd Floor slab work to be Complete
- S32/H10-3rd Floor slab work to be Complete
- S34/H8-1st Floor slab work to be Complete
- S35/H7-1st Floor slab work to be Complete

CLUSTER J (J17/N49 TO J20/N52)



Actual site photograph

CLUSTER J STATUS

- N49- Plinth beam work in progress.
- N50- GF Column work in progress
- N51- GF Column work in progress
- N52- Plinth beam completed & grade slab work in progress.



MILESTONES ACHIEVED

- N50/J17-Plinth beam completed.
- N52/J20-Plinth beam completed.



UPCOMING MILESTONES

- N49/J17-Plinth beam work to be complete

PROGRESS TIMELINE



February '26

CLUSTER J (J16/N48 TO J10/N42)



Actual site photograph

PROGRESS TIMELINE



February'26

CLUSTER J STATUS

- N-48- Plinth beam PCC Work in progress.
- N-47 -Footing work completed & Back filling work in progress
- N-46 -Footing work completed & Back filling work in progress
- N-45-Footing work completed & Back filling work in progress
- N-44 -Footing work completed & Back filling work in progress
- N-43 -Footing work completed & Back filling work in progress
- N-42 -Footing work completed & Back filling work in progress



MILESTONES ACHIEVED



UPCOMING MILESTONES

- N48/J16-Plinth beam work to be complete
- N47/J15-Plinth beam work to be complete

CLUSTER J (J09/N41 TO J01/N33)



Actual site photograph

PROGRESS TIMELINE



February'26

CLUSTER J STATUS

- N41- Footing work completed & Back filling work in progress
- N40- Footing work completed & Back filling work in progress
- N39- Footing work completed & Back filling work in progress
- N38- Plinth beam PCC work in progress.
- N37- Plinth beam completed.
- N36- GF Column work completed.
- N35- 1st Floor slab completed.
- N34-1st Floor slab completed.
- N33- Plinth beam work in progress



MILESTONES ACHIEVED

- N34/J02- 1st floor slab completed.
- N35/J03- 1st floor slab completed.
- N37/J05-Plinth beam work completed



UPCOMING MILESTONES

- N33/J1-Plinth beam work to be complete
- N38/J6- Plinth beam work to be Complete
- N33/J- 1st Floor slab work to be Complete
- N36/J04- 1st floor slab work to be completed

CLUSTER F (F1/N20 TO F7/N26)



Actual site photograph

CLUSTER J STATUS

- N20- Excavation completed.
- N21- Footing work completed & Backfilling work in progress.
- N22- Footing work completed .
- N23-Footing work completed
- N24- Footing work in progress
- N25- Excavation work in progress



MILESTONES ACHIEVED

- N20/F01-Excavation work completed



UPCOMING MILESTONES

- N20/F01-Plinth beam work to be completed
- N25/F06-Excavation work to be completed.
- N26/F07-Excavation work to be completed

PROGRESS TIMELINE



February'26

Contact Us



Site Office :

Provident Deansgate

Uganawadi circle, Devanahalli Taluk,
Bengaluru – 562110.

Regional Office :

Provident Housing Limited

No.8, Ulsoor Road, Bengaluru- 560 042

Tel: 080-4455544

Email : crm@providenthousing.com (Subject line – Project name/ unit number)

Call Us : +91 - 80-67724001 / 1 860 208 0000

Web : www.providenthousing.com

RERA Registration Number :

RERA Nos.: PRM/KA/RERA/1250/303/PR/170325/007590
